




# MOUNTAIN VIEW WHISMAN SCHOOL DISTRICT

Measure T Construction Projects  
Master Plan Schedule


2020



2024

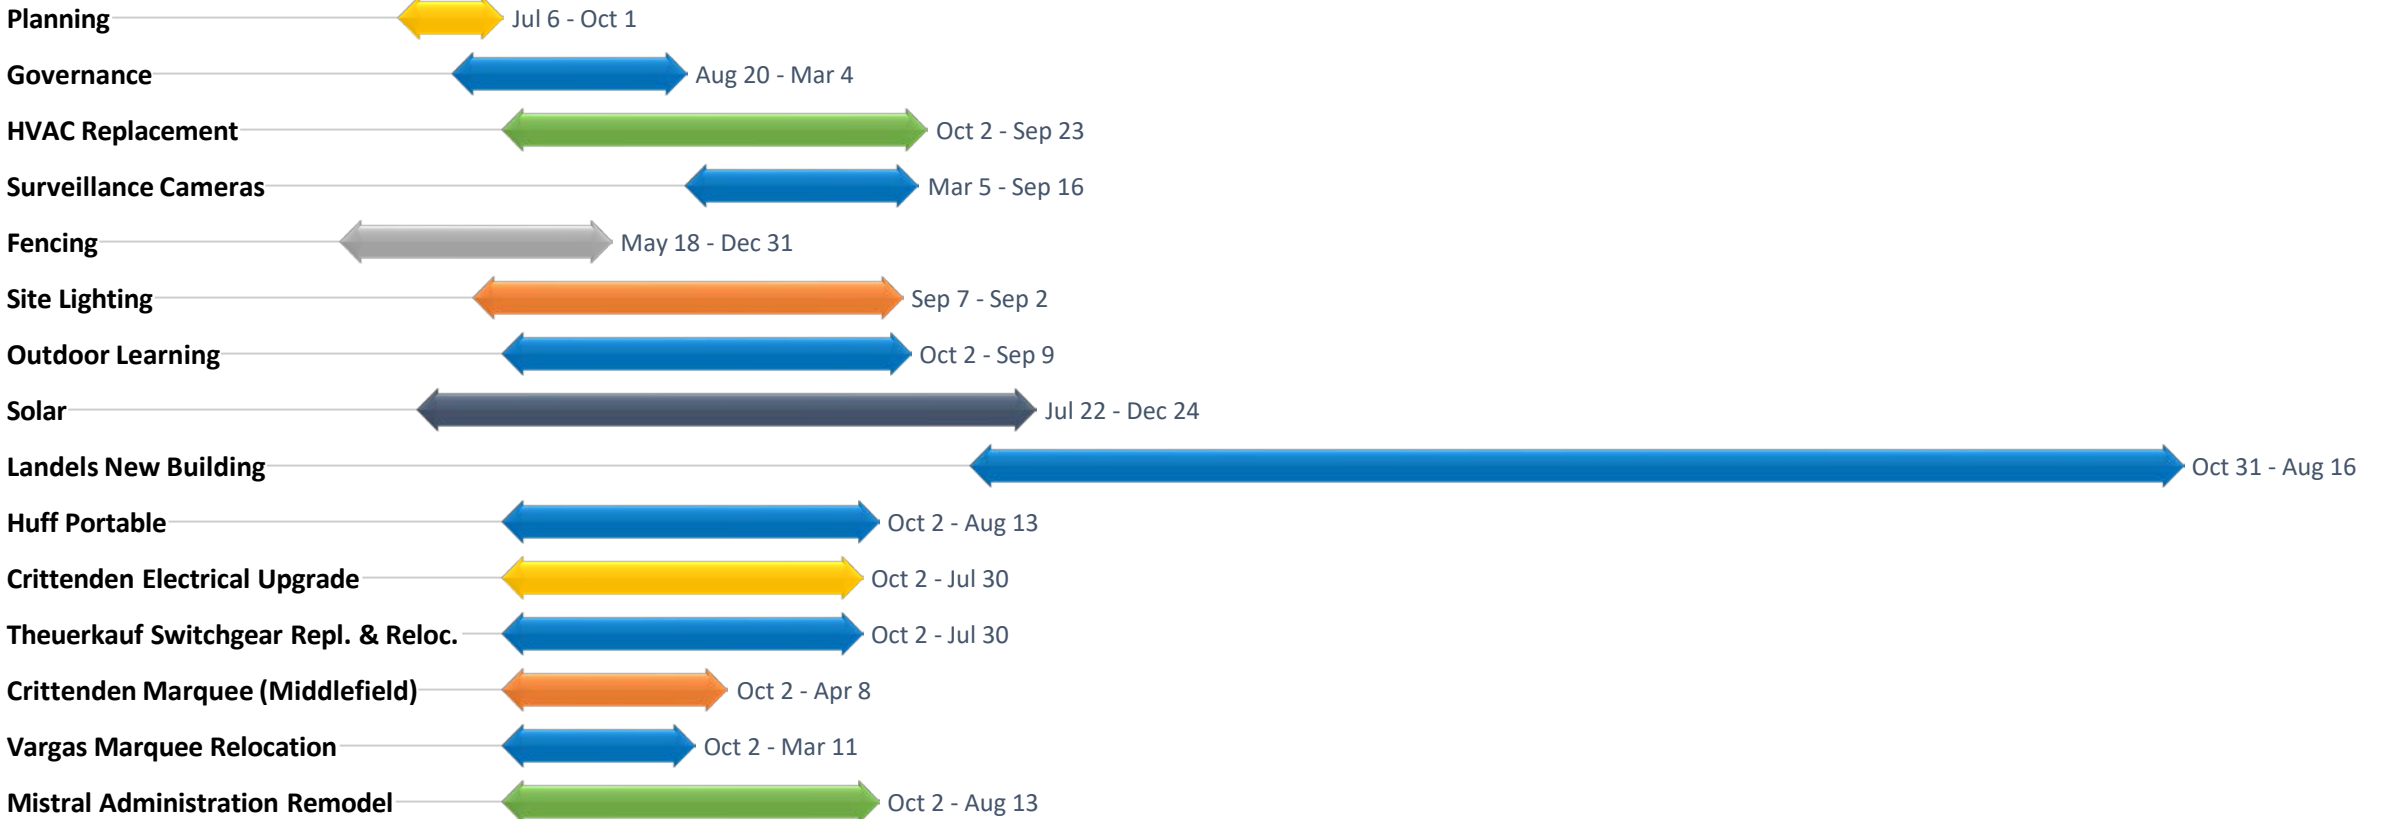


2020



2020

# Planning

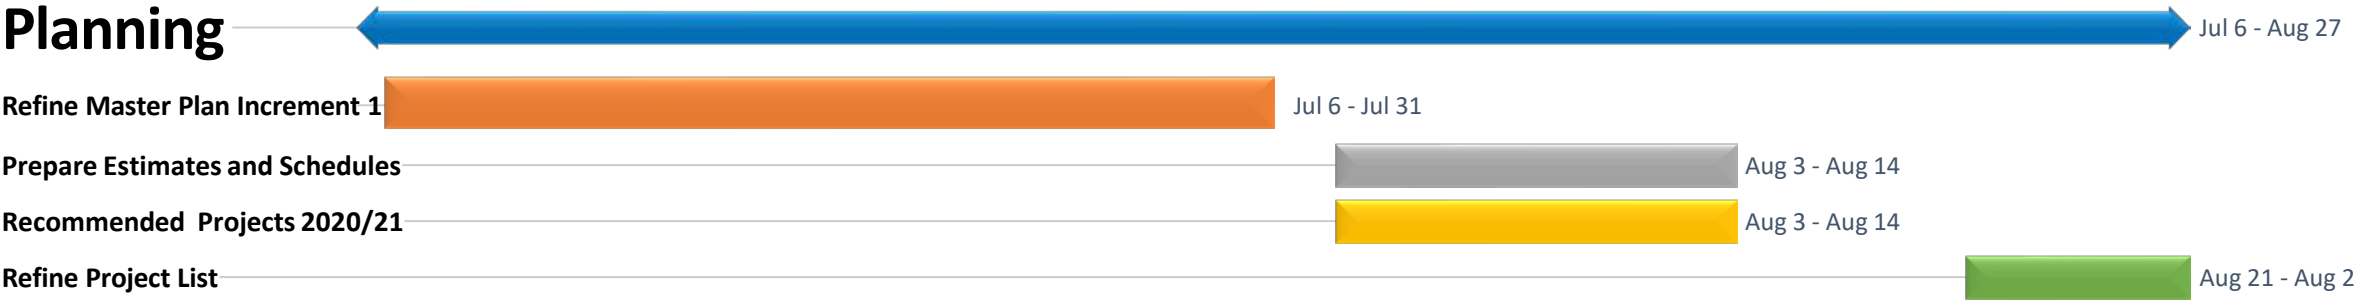

2020

2021



Aug 20 - Mar 4

# Governance

BOT Info Project List — Aug 20

BOT Info Camera Policy — Mar 4

BOT Action Architect Pool — Aug 20

BOT Action Consultant RFP's — Aug 20

BOT Action Project List — Sep 3

BOT Action Arch Assignments — Sep 3

2020



2021



Sep 4 - Aug 26

# HVAC Replacement

Schematic Design Sep 4 - Oct 1

BOT Action SD Approval Oct 1

Design Development Oct 2 - Nov 12

Petition DSA Nov 13 - Dec 3

Construction Documents Nov 13 - Dec 10


DSA Review (Full Review) Dec 4 - Apr 22

Order Equipment Feb 26

Bid and Award Apr 23 - Jun 10

Construction Jun 11 - Aug 26


2020



2020

# Fencing

May 18 - Dec 31

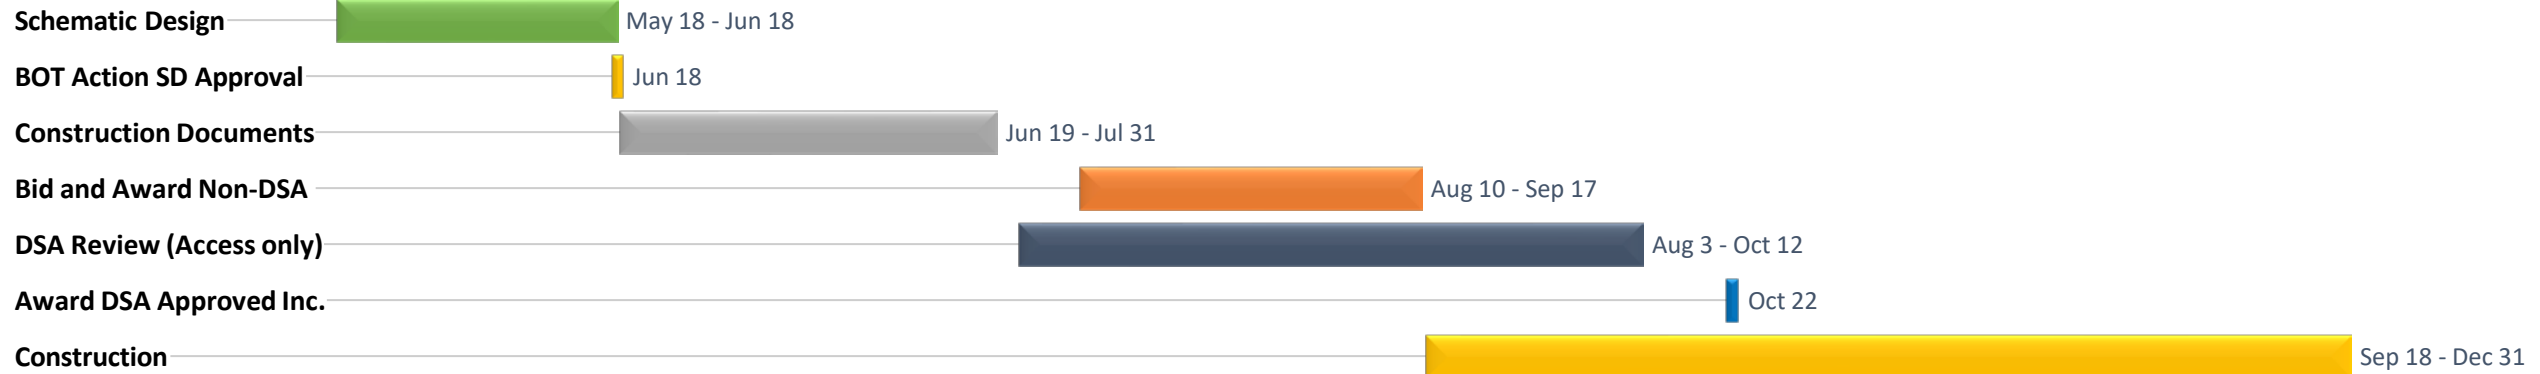

2021



2021



Mar 5 - Sep 16


# Surveillance Cameras

Schematic Design  Mar 5 - Mar 25

BOT Action SD Approval  Apr 1


Construction Documents  Apr 2 - May 13

Bid and Award  May 14 - Jun 24

Construction  Jun 25 - Sep 16


2020

2021



Aug 21 - Aug 5

# Site Lighting

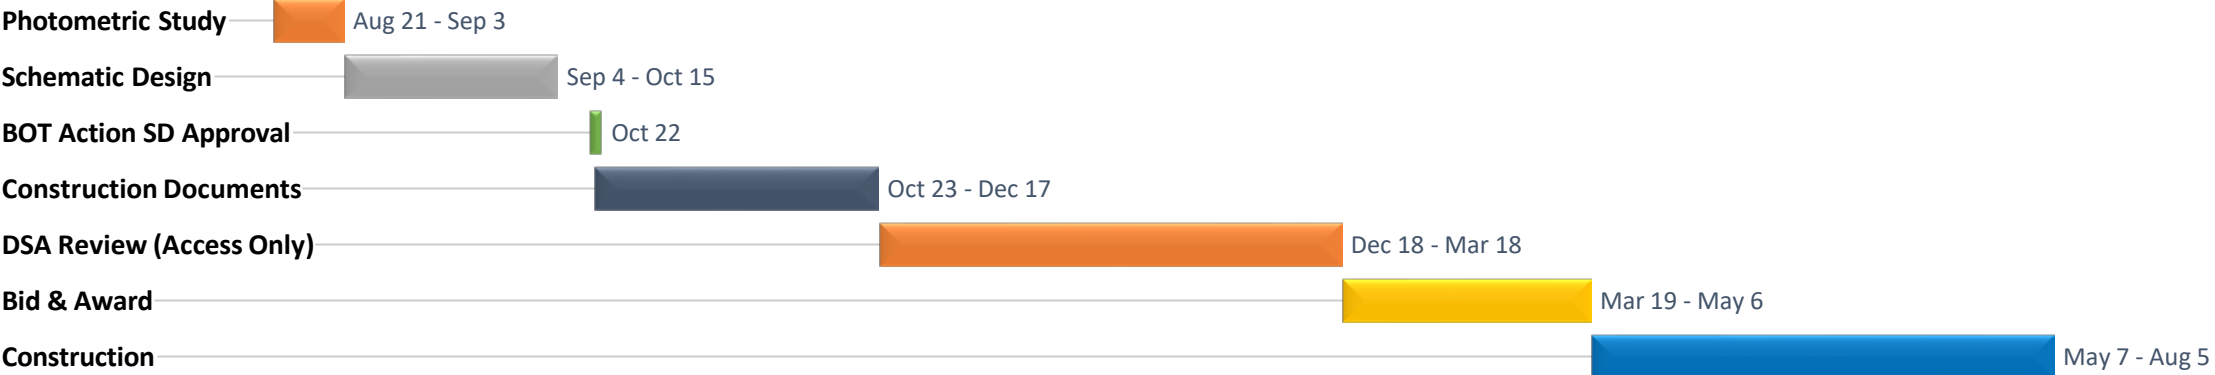



2020

2021



# Outdoor Learning

Sep 4 - May 27

Schematic Design  Sep 4 - Oct 1

BOT Action SD Approval  Oct 1

Construction Documents  Oct 2 - Nov 26


DSA Review (Access Only)  Nov 27 - Feb 18

Bid & Award  Jan 15 - Mar 4

Construction  Mar 5 - May 27


2020

2021



# Solar

Jul 22 - Dec 10

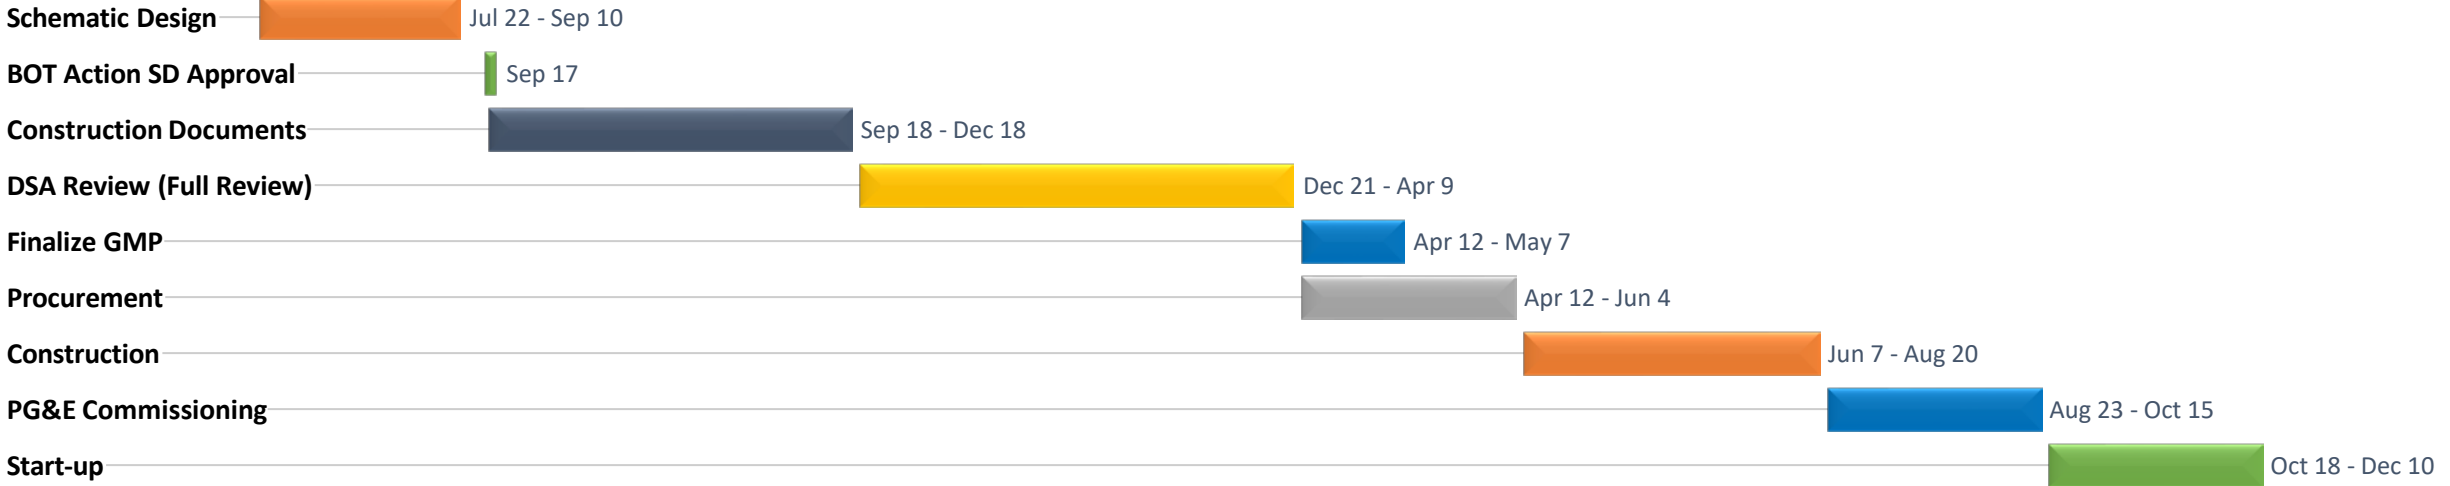

2021




2024



Oct 31 - Aug 16


# Landels New Building

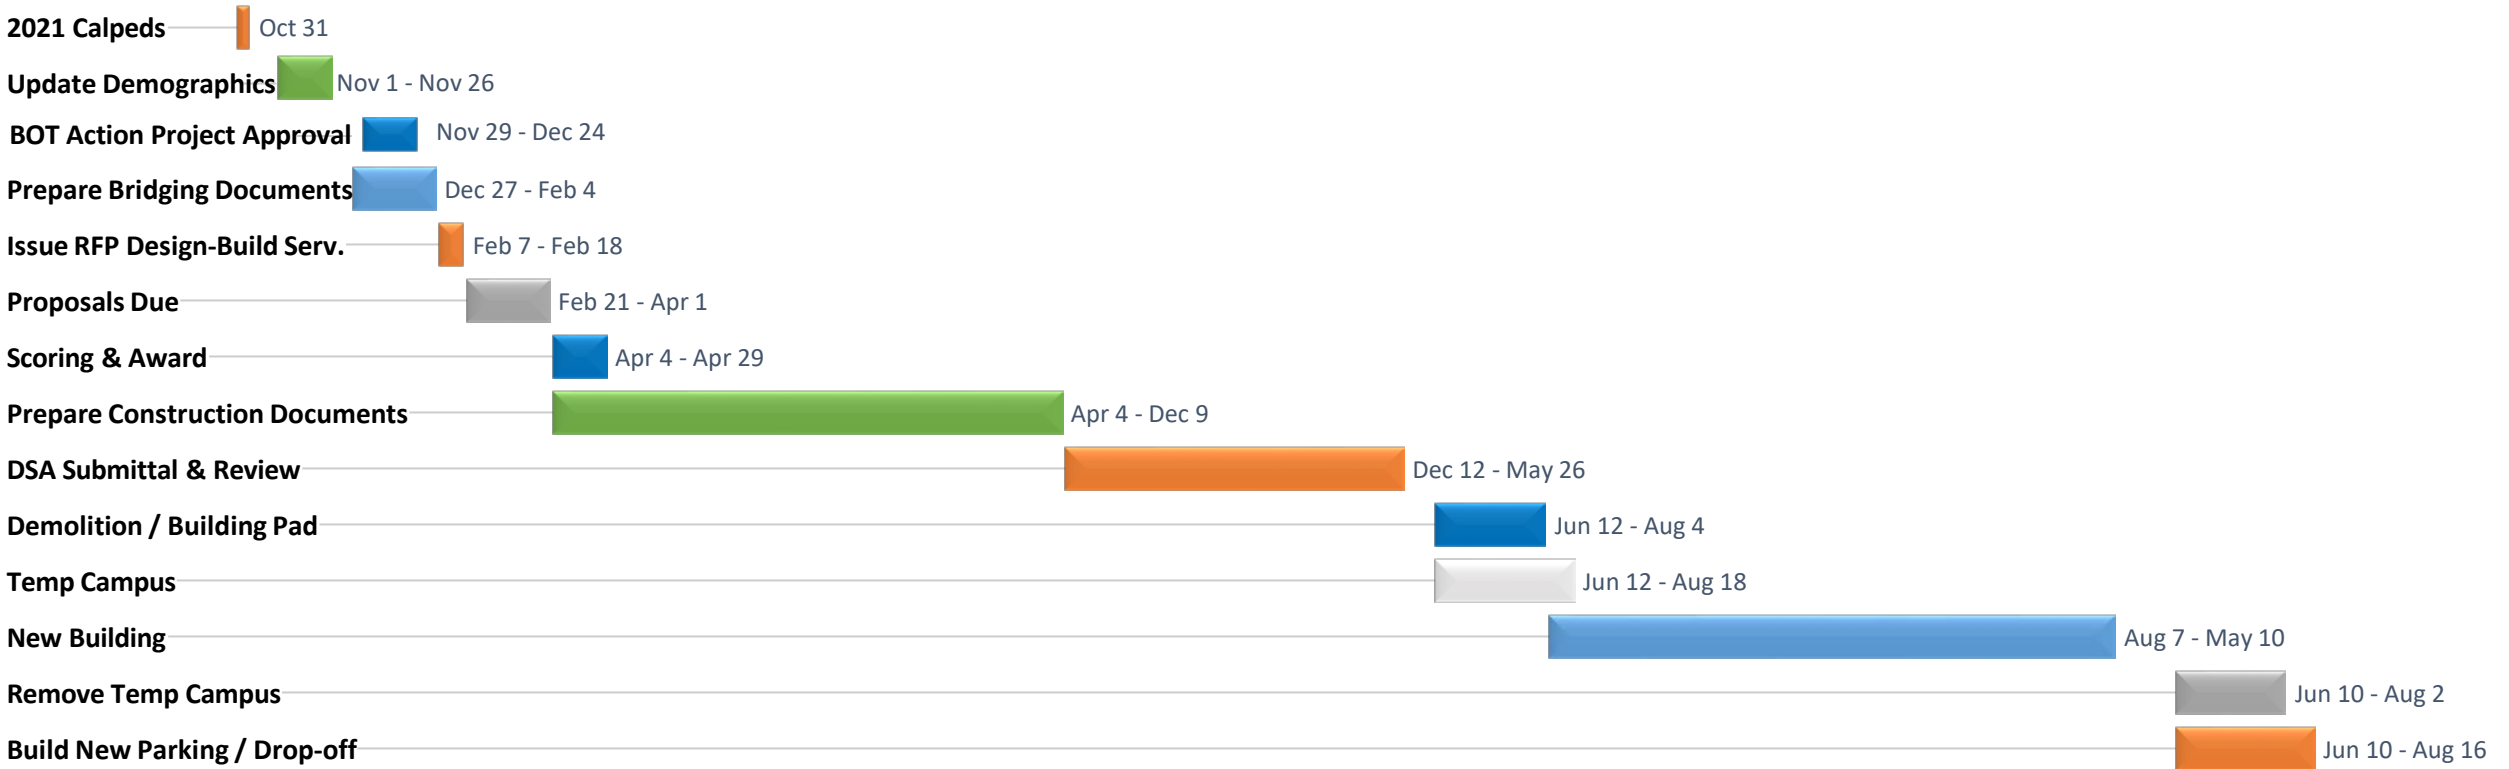

2020




2021



Sep 4 - Aug 13

# Huff Portable

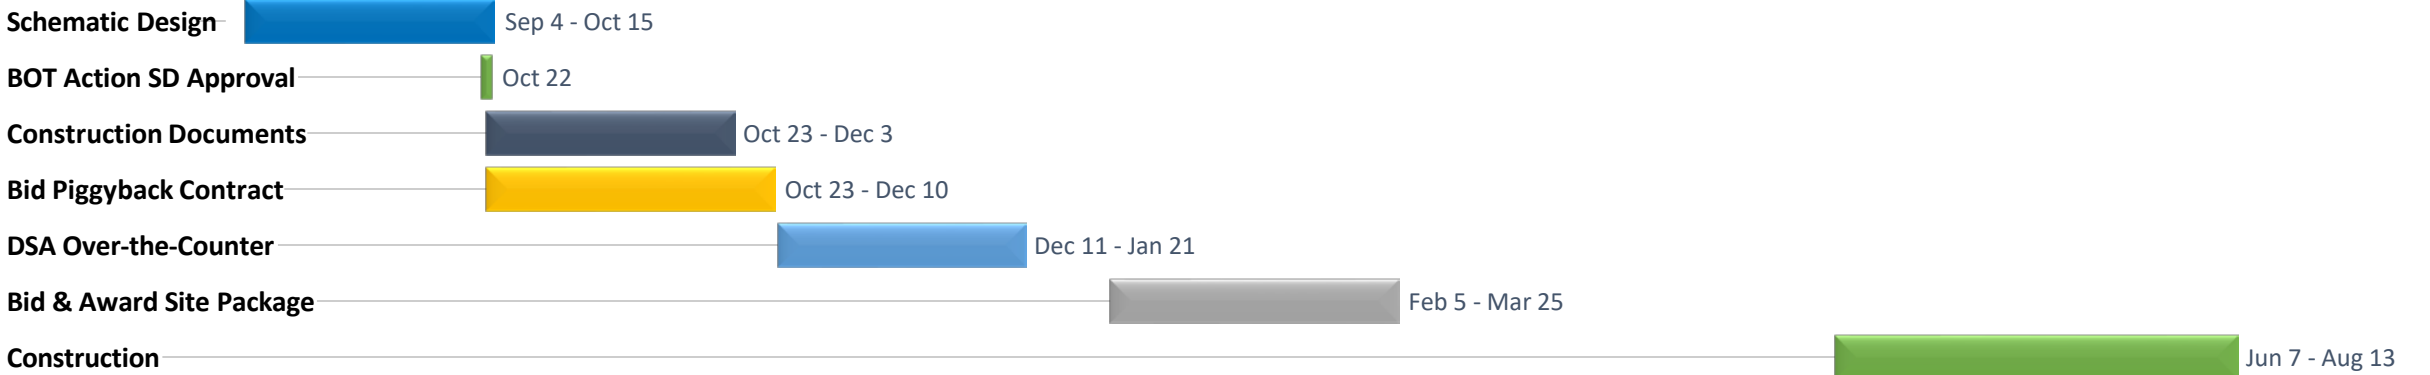

2020



2021



# Crittenden Electrical Upgrade

Sep 4 - Jul 30

**Schematic Design** Sep 4 - Oct 15



**BOT Action SD Approval** Oct 22



**Construction Documents** Oct 23 - Dec 3



**Bid and Award** Dec 4 - Jan 28



**Construction** Jun 7 - Jul 30



2020




2021



# Theuerkauf Switchgear Replacement and Relocation

Sep 4 - Jul 30

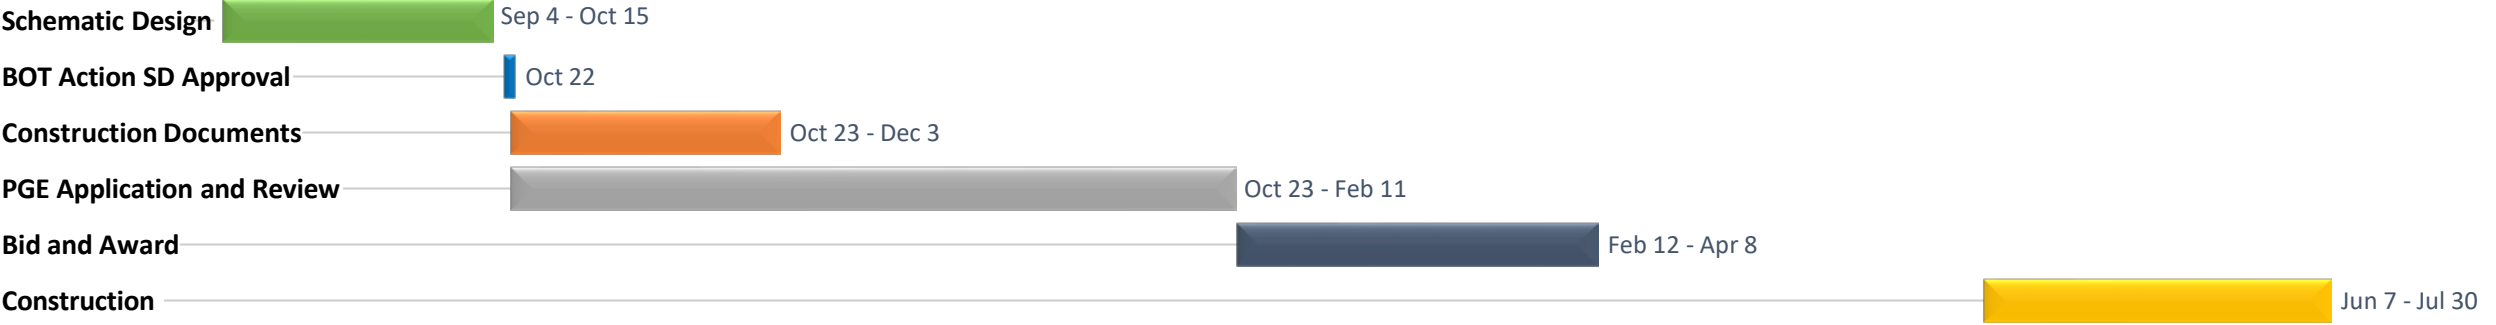

2020

2021



# Crittenden Marquee (Middlefield)

Oct 2 - Apr 8


Schematic Design Oct 2 - Nov 12

BOT Action SD Approval Nov 19

Construction Documents Nov 20 - Dec 31

Bid and Award Jan 1 - Feb 11

Construction Feb 26 - Apr 8

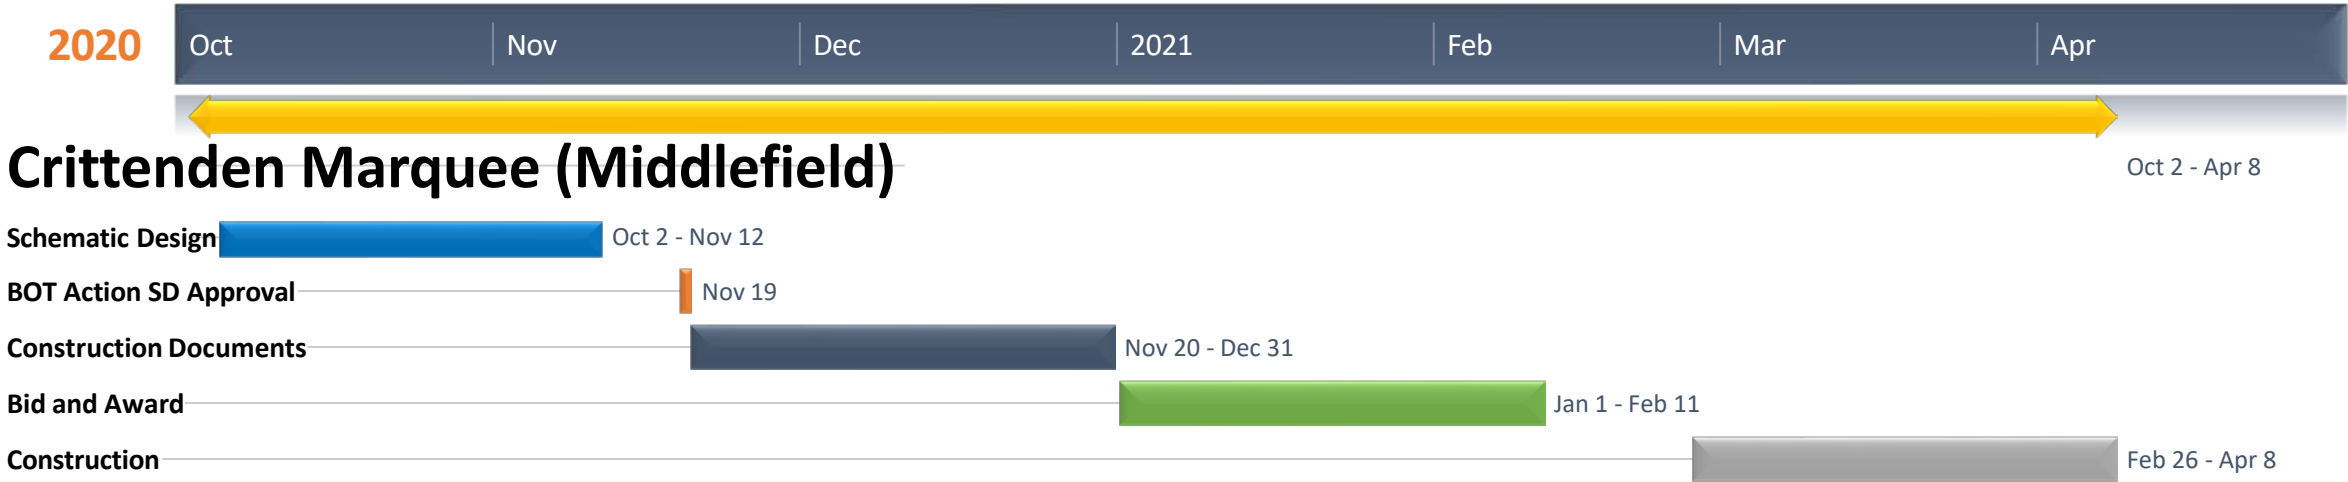

2020

2021



Oct 2 - Mar 11

# Vargas Marquee Relocation

Schematic Design Oct 2 - Oct 29

BOT Action SD Approval Nov 5

Construction Documents Nov 6 - Dec 3

Bid and Award Dec 4 - Jan 14

Construction Jan 29 - Mar 11



2020




2021



# Mistral Administration Remodel

Oct 2 - Aug 13

Reopen Project with DSA  Oct 2 - Dec 3

Bid and Award  Dec 4 - Jan 14

Construction  Jun 7 - Aug 13
