



Mountain View  
Whisman  
School District

# Measure T Phase 1 Construction Update

May 5, 2022



Mountain View  
Whisman  
School District

# Board Goals

# Strategic Plan 2021

## Goal 5 Resource Stewardship

- Goal 5: Students, staff and community members will have access to various resources, such as technology, facilities, furniture, equipment, etc., in a fiscally responsible manner, to fulfill the mission of MVWSD.

# Strategic Plan 2027

## Goal Area 5 Equitable Distribution of Resources that Support Student Success

- Goal 5a: Ensure facilities and resources equitably serve all students



Mountain View  
Whisman  
School District

# Master Facility Plan

# Master Facilities Plan

- Board approved a 10-year master facilities plan that accommodates growth while prioritizing the work ahead based on needs and input.
- The plan was approved on December 12th, 2019 prior to Measure T passing.
- New MFP continues the planning efforts of the former 2010 plan
- Solid foundation for student growth and upgrades to infrastructure
- Informs Bond Measure T

# Master Facilities Plan Feedback

- All schools' stakeholders met to discuss the Master Facility Plan
  - All school communities discussed potential solutions
    - New schools in North Bayshore & East Whisman
    - Reuse leased properties
    - Expand capacity of existing schools
    - Redraw school boundaries
    - Grade level schools
- Includes feedback from community in online ThoughtExchange

# Master Facilities Plan

- MFP describes how MVWSD will modernize and utilize existing school campuses for:
  - Safety and operational efficiency
  - Short-term growth
  - Long-term growth



Mountain View  
Whisman  
School District

# Measure T

# Funding the Master Facilities Plan

- March 3, 2020 Bond Measure T could be spent on:
  - Growth, Safety, Operational Efficiency
  - Short-term growth solutions
  - Staff housing
  - Repayment of Vargas Elementary construction
- Bond language is limited to 75 words and is broadly written to incorporate any projects that may be needed



Mountain View  
Whisman  
School District

# Facilities Priorities:

Short-term growth, operational  
efficiency and safety

# What Does This Mean for Our Schools?

Even though MFP identifies many projects to be done in the next 10 years, MVWSD has limited bond capacity. The MFP prioritizes:

- Safety and operational efficiency projects planned for all schools
  - Projects address facility needs identified in 2010
  - Some address evolving priorities
  - Short-term growth projects are proposed where substantial growth is occurring



Mountain View  
Whisman  
School District

# Update: Summer 2022 Measure T Projects by Site

# Bubb Elementary School

## Paving and Utilities

- Onsite work scheduled to begin in June and will include resurfacing and restriping of existing blacktop play space and seal coat of existing asphalt between classroom wings.

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

# Bubb (cont'd)

## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.


## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.





# Bubb Site Lighting

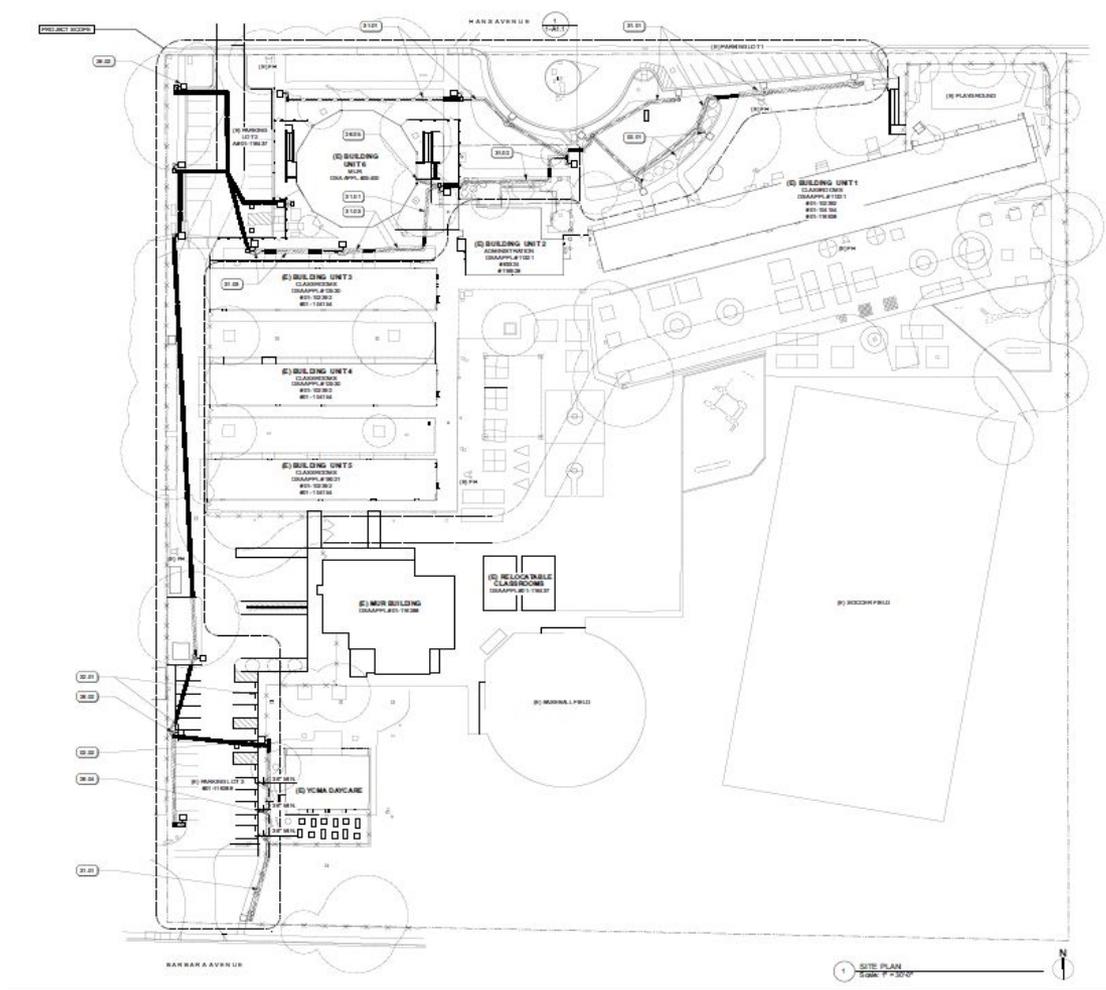

**KEYNOTES**

|      |                                 |
|------|---------------------------------|
| 1.00 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.01 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.02 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.03 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.04 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.05 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.06 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.07 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.08 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.09 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.10 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.11 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.12 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.13 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.14 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.15 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.16 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.17 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.18 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.19 | SEE KEYNOTES FOR SPECIFICATIONS |
| 1.20 | SEE KEYNOTES FOR SPECIFICATIONS |

**BENJAMIN BUBB ELEMENTARY SCHOOL**  
SITE LIGHTING

525 HARRIS AVE  
MOUNTAIN VIEW, CALIFORNIA

**MOUNTAIN VIEW WHISMAN SCHOOL DISTRICT**

1400 MONTICELLO AVE  
MOUNTAIN VIEW, CALIFORNIA  
(951) 558-3550

**HAMILTON + ATKEN ARCHITECTS**  
1400 MONTICELLO AVE  
MOUNTAIN VIEW, CALIFORNIA  
951-558-3550  
www.hamilton-aten.com

**HA ARCHITECTS**

**SHEET NOTES**

1. CONTRACTOR TO VERIFY ALL DIMENSIONS AND LOCATIONS OF ALL UTILITIES AND STRUCTURES BEFORE CONSTRUCTION.
2. ALL DIMENSIONS ARE TO FACE UNLESS OTHERWISE NOTED.
3. ALL DIMENSIONS ARE TO FACE UNLESS OTHERWISE NOTED.
4. ALL DIMENSIONS ARE TO FACE UNLESS OTHERWISE NOTED.

| NO. | DESCRIPTION       | DATE       |
|-----|-------------------|------------|
| 1   | ISSUED FOR PERMIT | 08/15/2017 |
| 2   | ISSUED FOR PERMIT | 08/15/2017 |
| 3   | ISSUED FOR PERMIT | 08/15/2017 |
| 4   | ISSUED FOR PERMIT | 08/15/2017 |
| 5   | ISSUED FOR PERMIT | 08/15/2017 |
| 6   | ISSUED FOR PERMIT | 08/15/2017 |
| 7   | ISSUED FOR PERMIT | 08/15/2017 |
| 8   | ISSUED FOR PERMIT | 08/15/2017 |
| 9   | ISSUED FOR PERMIT | 08/15/2017 |
| 10  | ISSUED FOR PERMIT | 08/15/2017 |
| 11  | ISSUED FOR PERMIT | 08/15/2017 |
| 12  | ISSUED FOR PERMIT | 08/15/2017 |
| 13  | ISSUED FOR PERMIT | 08/15/2017 |
| 14  | ISSUED FOR PERMIT | 08/15/2017 |
| 15  | ISSUED FOR PERMIT | 08/15/2017 |
| 16  | ISSUED FOR PERMIT | 08/15/2017 |
| 17  | ISSUED FOR PERMIT | 08/15/2017 |
| 18  | ISSUED FOR PERMIT | 08/15/2017 |
| 19  | ISSUED FOR PERMIT | 08/15/2017 |
| 20  | ISSUED FOR PERMIT | 08/15/2017 |
| 21  | ISSUED FOR PERMIT | 08/15/2017 |
| 22  | ISSUED FOR PERMIT | 08/15/2017 |
| 23  | ISSUED FOR PERMIT | 08/15/2017 |
| 24  | ISSUED FOR PERMIT | 08/15/2017 |
| 25  | ISSUED FOR PERMIT | 08/15/2017 |
| 26  | ISSUED FOR PERMIT | 08/15/2017 |
| 27  | ISSUED FOR PERMIT | 08/15/2017 |
| 28  | ISSUED FOR PERMIT | 08/15/2017 |
| 29  | ISSUED FOR PERMIT | 08/15/2017 |
| 30  | ISSUED FOR PERMIT | 08/15/2017 |
| 31  | ISSUED FOR PERMIT | 08/15/2017 |
| 32  | ISSUED FOR PERMIT | 08/15/2017 |
| 33  | ISSUED FOR PERMIT | 08/15/2017 |
| 34  | ISSUED FOR PERMIT | 08/15/2017 |
| 35  | ISSUED FOR PERMIT | 08/15/2017 |
| 36  | ISSUED FOR PERMIT | 08/15/2017 |
| 37  | ISSUED FOR PERMIT | 08/15/2017 |
| 38  | ISSUED FOR PERMIT | 08/15/2017 |
| 39  | ISSUED FOR PERMIT | 08/15/2017 |
| 40  | ISSUED FOR PERMIT | 08/15/2017 |
| 41  | ISSUED FOR PERMIT | 08/15/2017 |
| 42  | ISSUED FOR PERMIT | 08/15/2017 |
| 43  | ISSUED FOR PERMIT | 08/15/2017 |
| 44  | ISSUED FOR PERMIT | 08/15/2017 |
| 45  | ISSUED FOR PERMIT | 08/15/2017 |
| 46  | ISSUED FOR PERMIT | 08/15/2017 |
| 47  | ISSUED FOR PERMIT | 08/15/2017 |
| 48  | ISSUED FOR PERMIT | 08/15/2017 |
| 49  | ISSUED FOR PERMIT | 08/15/2017 |
| 50  | ISSUED FOR PERMIT | 08/15/2017 |

**LEGEND**

- PROPERTY LINE
- EXISTING PAVEMENT
- NEW PAVEMENT
- EXISTING SIDEWALK
- NEW SIDEWALK
- EXISTING DRIVEWAY
- NEW DRIVEWAY
- EXISTING FENCE
- NEW FENCE
- EXISTING UTILITY
- NEW UTILITY
- EXISTING TREE
- NEW TREE
- EXISTING PLANT
- NEW PLANT
- EXISTING LIGHT
- NEW LIGHT
- EXISTING SIGN
- NEW SIGN
- EXISTING WALL
- NEW WALL
- EXISTING ROOF
- NEW ROOF
- EXISTING FLOOR
- NEW FLOOR
- EXISTING CEILING
- NEW CEILING
- EXISTING DOOR
- NEW DOOR
- EXISTING WINDOW
- NEW WINDOW
- EXISTING STAIR
- NEW STAIR
- EXISTING ELEVATOR
- NEW ELEVATOR
- EXISTING MECHANICAL
- NEW MECHANICAL
- EXISTING ELECTRICAL
- NEW ELECTRICAL
- EXISTING PLUMBING
- NEW PLUMBING
- EXISTING HVAC
- NEW HVAC
- EXISTING FIRE
- NEW FIRE
- EXISTING SECURITY
- NEW SECURITY
- EXISTING ACCESSIBILITY
- NEW ACCESSIBILITY
- EXISTING SLOPE
- NEW SLOPE
- EXISTING GRADE
- NEW GRADE
- EXISTING EROSION CONTROL
- NEW EROSION CONTROL
- EXISTING DRAINAGE
- NEW DRAINAGE
- EXISTING IRRIGATION
- NEW IRRIGATION
- EXISTING LANDSCAPE
- NEW LANDSCAPE
- EXISTING SITEWORK
- NEW SITEWORK
- EXISTING UTILITIES
- NEW UTILITIES
- EXISTING STRUCTURES
- NEW STRUCTURES
- EXISTING INFRASTRUCTURE
- NEW INFRASTRUCTURE
- EXISTING SERVICES
- NEW SERVICES
- EXISTING UTILITIES
- NEW UTILITIES
- EXISTING STRUCTURES
- NEW STRUCTURES
- EXISTING INFRASTRUCTURE
- NEW INFRASTRUCTURE
- EXISTING SERVICES
- NEW SERVICES

# Castro Elementary School

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.


## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction schedule is June 2022 to August 2022.

# Castro Surveillance Camera Project

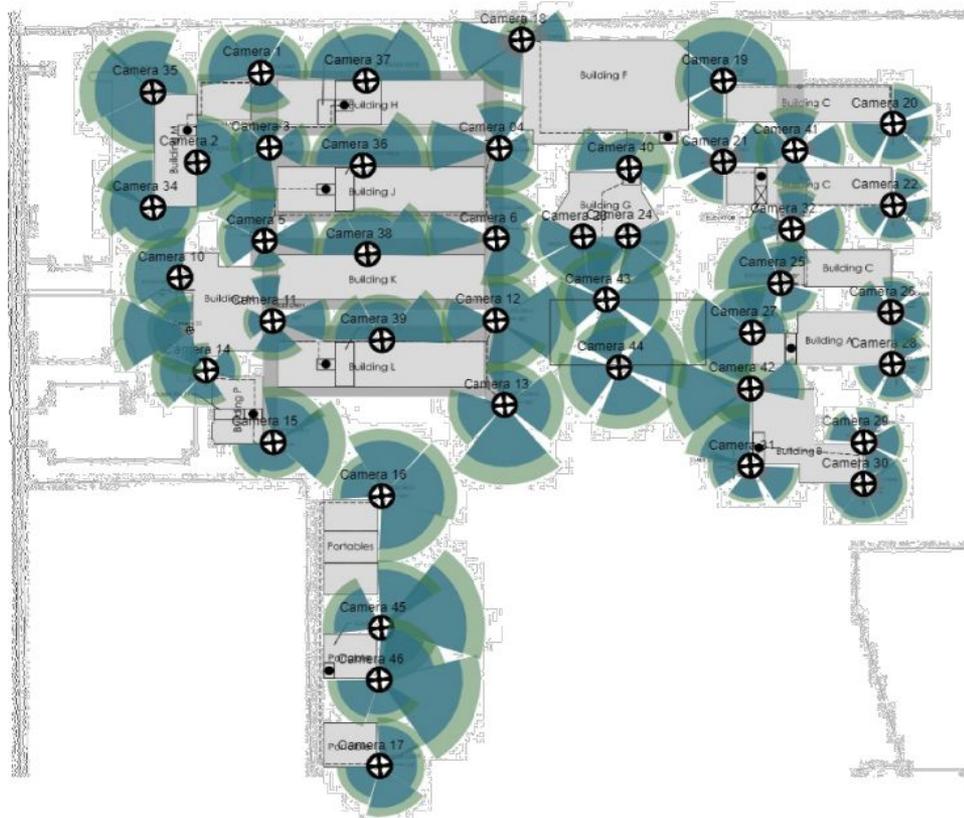

**Guidepost**  
 18000 Ave  
 Suite 100  
 San Jose, CA 95131  
 Phone: (415) 353-1100  
 Fax: (415) 353-1101  
 www.guidepost.com

ANALYSIS: COMMERCIAL DESIGN  
 CONSULTING: CALIFORNIA  
 REGISTERED PROFESSIONAL ARCHITECTS  
 10000 AVENUE  
 SUITE 100, SAN JOSE, CALIFORNIA  
 95131  
 (415) 353-1100  
 (415) 353-1101  
 WWW.GUIDEPOST.COM

---

**MOUNTAIN VIEW WHISMAN  
 SD - CASTRO & MISTRAL**

CASTRO & MISTRAL  
 585 ESCUELA AVE.  
 MOUNTAIN VIEW, CA  
 94041

---

DATE: 10/20/11  
 TIME: 11:00 AM  
 PROJECT: CASTRO & MISTRAL  
 DRAWING: SURVEILLANCE CAMERA PROJECT

SCALE: 75% CD

DATE: 10/20/11  
 CASE NUMBER:  
 CHECKED BY:  
 DRAWN BY:  
 PLOT:



# Crittenden Middle School

## Solar Project

- Scope of work includes installation of rooftop and ground mounted solar arrays, one (1) EV charging station with 2 ports and associated equipment.
- Onsite work scheduled to begin in June 2022 and run through December 2022.

## HVAC Upgrades

- Replacement of existing HVAC units in classrooms and administration building.
- Scheduled for June 2022 to August 2022.

# Crittenden (cont'd)

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

# Crittenden (cont'd)

## Site Lighting


- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.

## Paving Project

- Scope of work includes demolition and repaving of a section of drive aisle and parking between Rock Street and the parking lot adjacent to the sports center.
- Construction scheduled for June 2022 to July 2022.



# Crittenden HVAC Upgrade

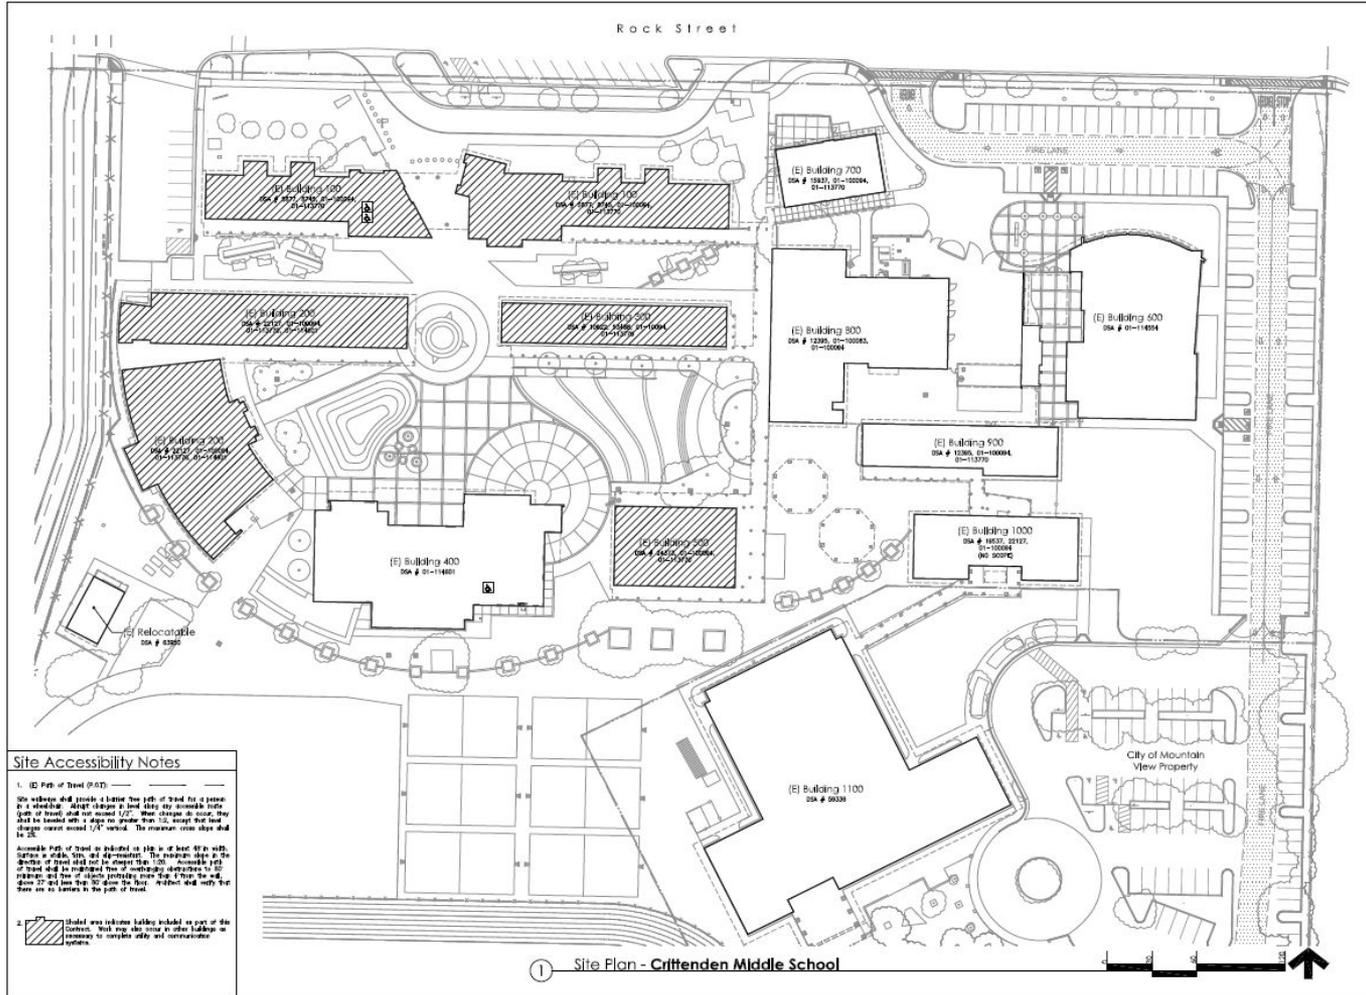


HVAC Modernization and Enhancement  
**Crittenden Middle School**  
 Mountain View, CA 94041

|                     |            |
|---------------------|------------|
| Site Program Rev    | 01/11/2023 |
| Site Layout Rev     | 01/11/2023 |
| Site Mechanical Rev | 01/11/2023 |
| Site Electrical Rev | 01/11/2023 |

Crittenden Middle School  
 Site Plan  
 AC1.1



# Crittenden Site Lighting Project

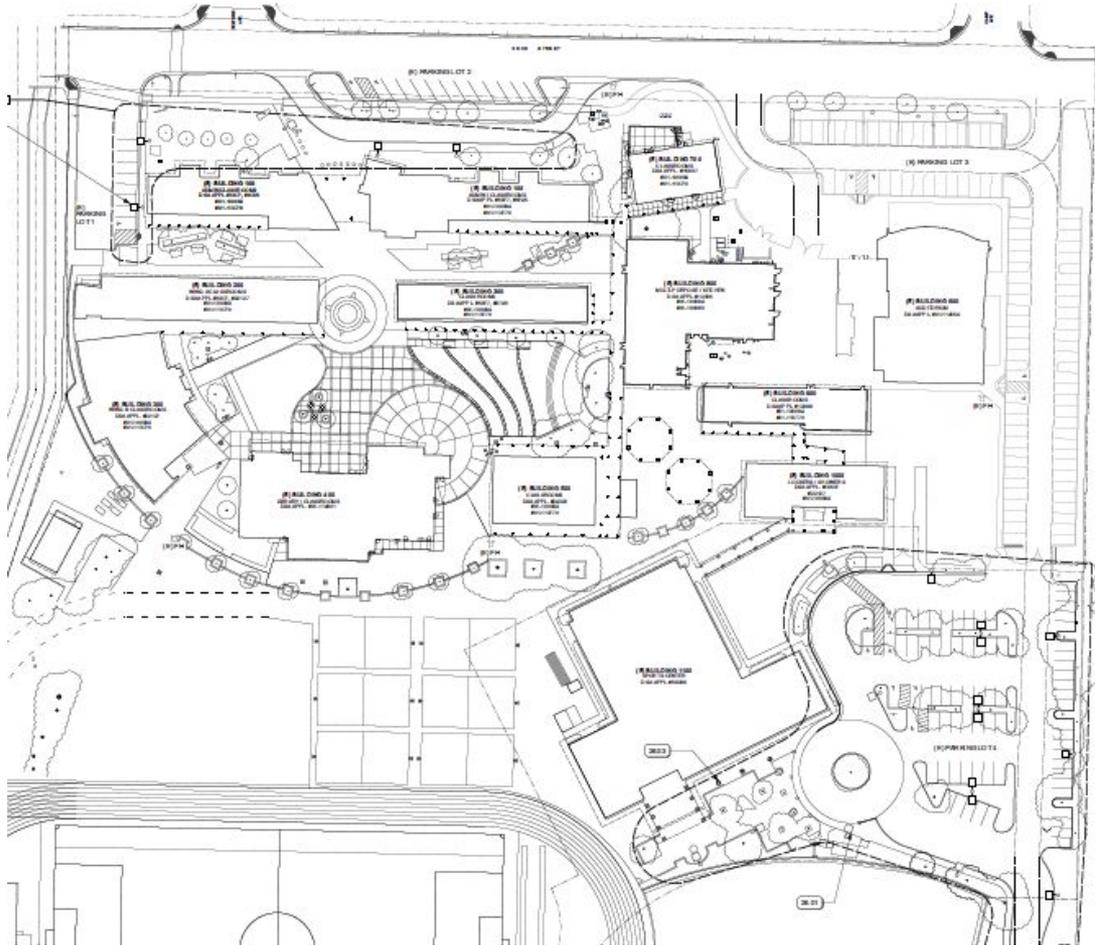

| KEYNOTES |                           |
|----------|---------------------------|
| KEY      | NOTE                      |
| 1        | OFFICE (SCHEDULED) (S.D.) |
| 2        | OFFICE (SCHEDULED) (S.D.) |
| 3        | OFFICE (SCHEDULED) (S.D.) |
| 4        | OFFICE (SCHEDULED) (S.D.) |
| 5        | OFFICE (SCHEDULED) (S.D.) |
| 6        | OFFICE (SCHEDULED) (S.D.) |
| 7        | OFFICE (SCHEDULED) (S.D.) |
| 8        | OFFICE (SCHEDULED) (S.D.) |
| 9        | OFFICE (SCHEDULED) (S.D.) |
| 10       | OFFICE (SCHEDULED) (S.D.) |
| 11       | OFFICE (SCHEDULED) (S.D.) |
| 12       | OFFICE (SCHEDULED) (S.D.) |
| 13       | OFFICE (SCHEDULED) (S.D.) |
| 14       | OFFICE (SCHEDULED) (S.D.) |
| 15       | OFFICE (SCHEDULED) (S.D.) |
| 16       | OFFICE (SCHEDULED) (S.D.) |
| 17       | OFFICE (SCHEDULED) (S.D.) |
| 18       | OFFICE (SCHEDULED) (S.D.) |
| 19       | OFFICE (SCHEDULED) (S.D.) |
| 20       | OFFICE (SCHEDULED) (S.D.) |
| 21       | OFFICE (SCHEDULED) (S.D.) |
| 22       | OFFICE (SCHEDULED) (S.D.) |
| 23       | OFFICE (SCHEDULED) (S.D.) |
| 24       | OFFICE (SCHEDULED) (S.D.) |
| 25       | OFFICE (SCHEDULED) (S.D.) |
| 26       | OFFICE (SCHEDULED) (S.D.) |
| 27       | OFFICE (SCHEDULED) (S.D.) |
| 28       | OFFICE (SCHEDULED) (S.D.) |
| 29       | OFFICE (SCHEDULED) (S.D.) |
| 30       | OFFICE (SCHEDULED) (S.D.) |
| 31       | OFFICE (SCHEDULED) (S.D.) |
| 32       | OFFICE (SCHEDULED) (S.D.) |
| 33       | OFFICE (SCHEDULED) (S.D.) |
| 34       | OFFICE (SCHEDULED) (S.D.) |
| 35       | OFFICE (SCHEDULED) (S.D.) |
| 36       | OFFICE (SCHEDULED) (S.D.) |
| 37       | OFFICE (SCHEDULED) (S.D.) |
| 38       | OFFICE (SCHEDULED) (S.D.) |
| 39       | OFFICE (SCHEDULED) (S.D.) |
| 40       | OFFICE (SCHEDULED) (S.D.) |
| 41       | OFFICE (SCHEDULED) (S.D.) |
| 42       | OFFICE (SCHEDULED) (S.D.) |
| 43       | OFFICE (SCHEDULED) (S.D.) |
| 44       | OFFICE (SCHEDULED) (S.D.) |
| 45       | OFFICE (SCHEDULED) (S.D.) |
| 46       | OFFICE (SCHEDULED) (S.D.) |
| 47       | OFFICE (SCHEDULED) (S.D.) |
| 48       | OFFICE (SCHEDULED) (S.D.) |
| 49       | OFFICE (SCHEDULED) (S.D.) |
| 50       | OFFICE (SCHEDULED) (S.D.) |
| 51       | OFFICE (SCHEDULED) (S.D.) |
| 52       | OFFICE (SCHEDULED) (S.D.) |
| 53       | OFFICE (SCHEDULED) (S.D.) |
| 54       | OFFICE (SCHEDULED) (S.D.) |
| 55       | OFFICE (SCHEDULED) (S.D.) |
| 56       | OFFICE (SCHEDULED) (S.D.) |
| 57       | OFFICE (SCHEDULED) (S.D.) |
| 58       | OFFICE (SCHEDULED) (S.D.) |
| 59       | OFFICE (SCHEDULED) (S.D.) |
| 60       | OFFICE (SCHEDULED) (S.D.) |
| 61       | OFFICE (SCHEDULED) (S.D.) |
| 62       | OFFICE (SCHEDULED) (S.D.) |
| 63       | OFFICE (SCHEDULED) (S.D.) |
| 64       | OFFICE (SCHEDULED) (S.D.) |
| 65       | OFFICE (SCHEDULED) (S.D.) |
| 66       | OFFICE (SCHEDULED) (S.D.) |
| 67       | OFFICE (SCHEDULED) (S.D.) |
| 68       | OFFICE (SCHEDULED) (S.D.) |
| 69       | OFFICE (SCHEDULED) (S.D.) |
| 70       | OFFICE (SCHEDULED) (S.D.) |
| 71       | OFFICE (SCHEDULED) (S.D.) |
| 72       | OFFICE (SCHEDULED) (S.D.) |
| 73       | OFFICE (SCHEDULED) (S.D.) |
| 74       | OFFICE (SCHEDULED) (S.D.) |
| 75       | OFFICE (SCHEDULED) (S.D.) |
| 76       | OFFICE (SCHEDULED) (S.D.) |
| 77       | OFFICE (SCHEDULED) (S.D.) |
| 78       | OFFICE (SCHEDULED) (S.D.) |
| 79       | OFFICE (SCHEDULED) (S.D.) |
| 80       | OFFICE (SCHEDULED) (S.D.) |
| 81       | OFFICE (SCHEDULED) (S.D.) |
| 82       | OFFICE (SCHEDULED) (S.D.) |
| 83       | OFFICE (SCHEDULED) (S.D.) |
| 84       | OFFICE (SCHEDULED) (S.D.) |
| 85       | OFFICE (SCHEDULED) (S.D.) |
| 86       | OFFICE (SCHEDULED) (S.D.) |
| 87       | OFFICE (SCHEDULED) (S.D.) |
| 88       | OFFICE (SCHEDULED) (S.D.) |
| 89       | OFFICE (SCHEDULED) (S.D.) |
| 90       | OFFICE (SCHEDULED) (S.D.) |
| 91       | OFFICE (SCHEDULED) (S.D.) |
| 92       | OFFICE (SCHEDULED) (S.D.) |
| 93       | OFFICE (SCHEDULED) (S.D.) |
| 94       | OFFICE (SCHEDULED) (S.D.) |
| 95       | OFFICE (SCHEDULED) (S.D.) |
| 96       | OFFICE (SCHEDULED) (S.D.) |
| 97       | OFFICE (SCHEDULED) (S.D.) |
| 98       | OFFICE (SCHEDULED) (S.D.) |
| 99       | OFFICE (SCHEDULED) (S.D.) |
| 100      | OFFICE (SCHEDULED) (S.D.) |

|  |              |          |
|--|--------------|----------|
| <b>CRITTENDEN MIDDLE SCHOOL</b>  |              |          |
| SITE LIGHTING  |              |          |
| 1701 ROCK ST.<br>MOUNTAIN VIEW, CA 94043   |              |          |
| <b>MOUNTAIN VIEW WHISMAN SCHOOL DISTRICT</b>   |              |          |
| 1400 MONTECITO AVE.<br>MOUNTAIN VIEW, CA 94043<br>(650) 538-3500   |              |          |
|  <b>HAMILTON + AIKEN ARCHITECTS</b><br>225 S. MONTECITO AVE. STE. 200<br>MOUNTAIN VIEW, CA 94043<br>TEL: 650-974-8888<br>WWW.HAARCHITECTS.COM |              |          |
|   |              |          |
| CONSTRUCTION   |              |          |
| NO.  | ISSUED FOR   | DATE     |
| 1  | CONSTRUCTION | 08/20/20 |
| 2  | CONSTRUCTION | 08/20/20 |
| 3  | CONSTRUCTION | 08/20/20 |
| 4  | CONSTRUCTION | 08/20/20 |
| 5  | CONSTRUCTION | 08/20/20 |
| 6  | CONSTRUCTION | 08/20/20 |
| 7  | CONSTRUCTION | 08/20/20 |
| 8  | CONSTRUCTION | 08/20/20 |
| 9  | CONSTRUCTION | 08/20/20 |
| 10   | CONSTRUCTION | 08/20/20 |
| 11   | CONSTRUCTION | 08/20/20 |
| 12   | CONSTRUCTION | 08/20/20 |
| 13   | CONSTRUCTION | 08/20/20 |
| 14   | CONSTRUCTION | 08/20/20 |
| 15   | CONSTRUCTION | 08/20/20 |
| 16   | CONSTRUCTION | 08/20/20 |
| 17   | CONSTRUCTION | 08/20/20 |
| 18   | CONSTRUCTION | 08/20/20 |
| 19   | CONSTRUCTION | 08/20/20 |
| 20   | CONSTRUCTION | 08/20/20 |
| 21   | CONSTRUCTION | 08/20/20 |
| 22   | CONSTRUCTION | 08/20/20 |
| 23   | CONSTRUCTION | 08/20/20 |
| 24   | CONSTRUCTION | 08/20/20 |
| 25   | CONSTRUCTION | 08/20/20 |
| 26   | CONSTRUCTION | 08/20/20 |
| 27   | CONSTRUCTION | 08/20/20 |
| 28   | CONSTRUCTION | 08/20/20 |
| 29   | CONSTRUCTION | 08/20/20 |
| 30   | CONSTRUCTION | 08/20/20 |
| 31   | CONSTRUCTION | 08/20/20 |
| 32   | CONSTRUCTION | 08/20/20 |
| 33   | CONSTRUCTION | 08/20/20 |
| 34   | CONSTRUCTION | 08/20/20 |
| 35   | CONSTRUCTION | 08/20/20 |
| 36   | CONSTRUCTION | 08/20/20 |
| 37   | CONSTRUCTION | 08/20/20 |
| 38   | CONSTRUCTION | 08/20/20 |
| 39   | CONSTRUCTION | 08/20/20 |
| 40   | CONSTRUCTION | 08/20/20 |
| 41   | CONSTRUCTION | 08/20/20 |
| 42   | CONSTRUCTION | 08/20/20 |
| 43   | CONSTRUCTION | 08/20/20 |
| 44   | CONSTRUCTION | 08/20/20 |
| 45   | CONSTRUCTION | 08/20/20 |
| 46   | CONSTRUCTION | 08/20/20 |
| 47   | CONSTRUCTION | 08/20/20 |
| 48   | CONSTRUCTION | 08/20/20 |
| 49   | CONSTRUCTION | 08/20/20 |
| 50   | CONSTRUCTION | 08/20/20 |
| 51   | CONSTRUCTION | 08/20/20 |
| 52   | CONSTRUCTION | 08/20/20 |
| 53   | CONSTRUCTION | 08/20/20 |
| 54   | CONSTRUCTION | 08/20/20 |
| 55   | CONSTRUCTION | 08/20/20 |
| 56   | CONSTRUCTION | 08/20/20 |
| 57   | CONSTRUCTION | 08/20/20 |
| 58   | CONSTRUCTION | 08/20/20 |
| 59   | CONSTRUCTION | 08/20/20 |
| 60   | CONSTRUCTION | 08/20/20 |
| 61   | CONSTRUCTION | 08/20/20 |
| 62   | CONSTRUCTION | 08/20/20 |
| 63   | CONSTRUCTION | 08/20/20 |
| 64   | CONSTRUCTION | 08/20/20 |
| 65   | CONSTRUCTION | 08/20/20 |
| 66   | CONSTRUCTION | 08/20/20 |
| 67   | CONSTRUCTION | 08/20/20 |
| 68   | CONSTRUCTION | 08/20/20 |
| 69   | CONSTRUCTION | 08/20/20 |
| 70   | CONSTRUCTION | 08/20/20 |
| 71   | CONSTRUCTION | 08/20/20 |
| 72   | CONSTRUCTION | 08/20/20 |
| 73   | CONSTRUCTION | 08/20/20 |
| 74   | CONSTRUCTION | 08/20/20 |
| 75   | CONSTRUCTION | 08/20/20 |
| 76   | CONSTRUCTION | 08/20/20 |
| 77   | CONSTRUCTION | 08/20/20 |
| 78   | CONSTRUCTION | 08/20/20 |
| 79   | CONSTRUCTION | 08/20/20 |
| 80   | CONSTRUCTION | 08/20/20 |
| 81   | CONSTRUCTION | 08/20/20 |
| 82   | CONSTRUCTION | 08/20/20 |
| 83   | CONSTRUCTION | 08/20/20 |
| 84   | CONSTRUCTION | 08/20/20 |
| 85   | CONSTRUCTION | 08/20/20 |
| 86   | CONSTRUCTION | 08/20/20 |
| 87   | CONSTRUCTION | 08/20/20 |
| 88   | CONSTRUCTION | 08/20/20 |
| 89   | CONSTRUCTION | 08/20/20 |
| 90   | CONSTRUCTION | 08/20/20 |
| 91   | CONSTRUCTION | 08/20/20 |
| 92   | CONSTRUCTION | 08/20/20 |
| 93   | CONSTRUCTION | 08/20/20 |
| 94   | CONSTRUCTION | 08/20/20 |
| 95   | CONSTRUCTION | 08/20/20 |
| 96   | CONSTRUCTION | 08/20/20 |
| 97   | CONSTRUCTION | 08/20/20 |
| 98   | CONSTRUCTION | 08/20/20 |
| 99   | CONSTRUCTION | 08/20/20 |
| 100  | CONSTRUCTION | 08/20/20 |

Mountain View Whisman School District



# Graham Middle School

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

## Surveillance Camera Project


- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.



# Graham Site Lighting

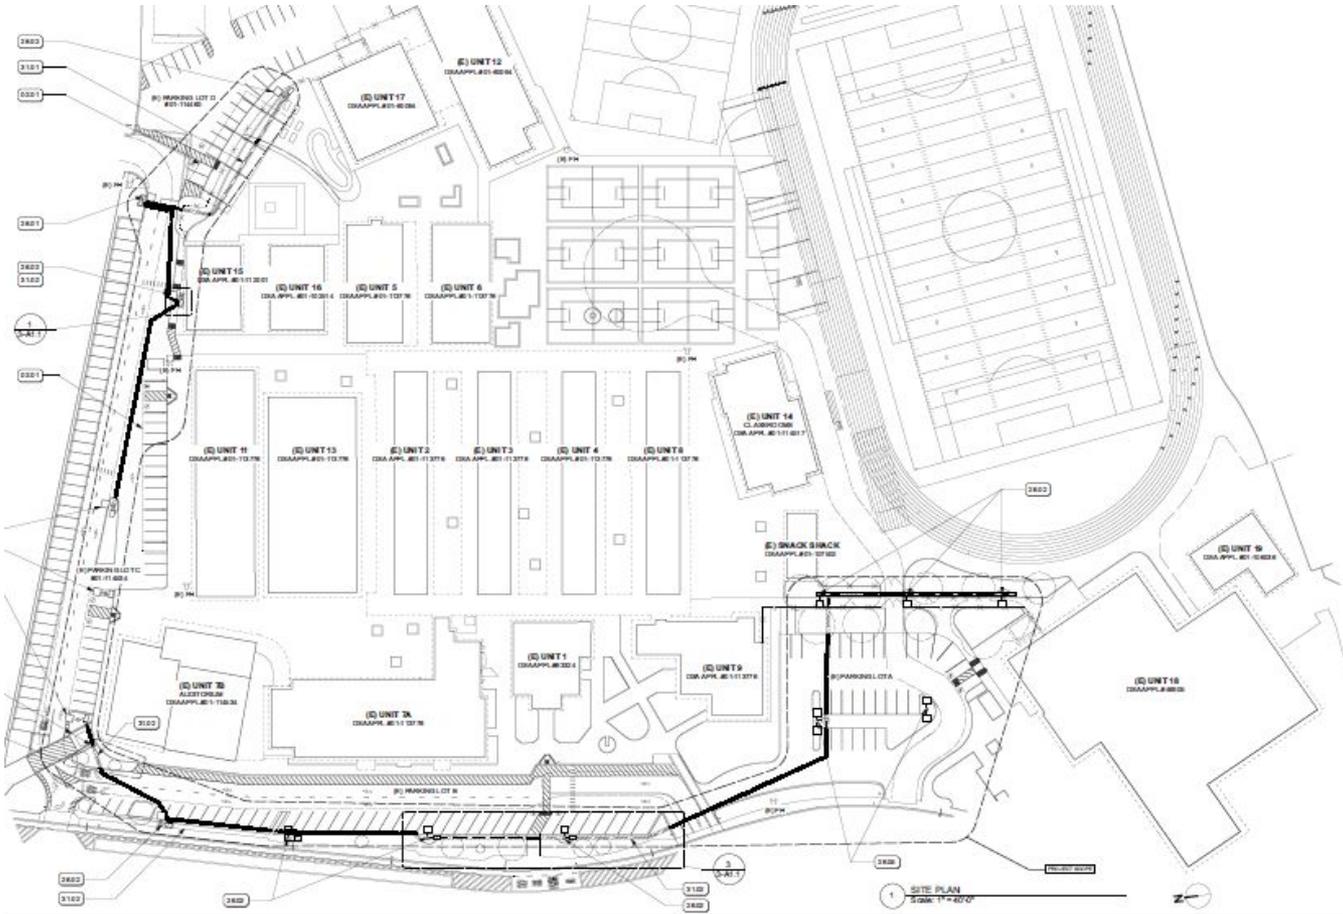

## GRAHAM MIDDLE SCHOOL

### SITE LIGHTING

1175 GASTRO ST  
MOUNTAIN VIEW, CA 94040

## MOUNTAIN VIEW WHISMAN SCHOOL DISTRICT

1400 MONTECITO AVE  
MOUNTAIN VIEW, CA 94040  
(925) 536-3500

### SHEET NOTES

1. CONTRACTOR TO PROVIDE AND/OR REPAIR AS NECESSARY.
2. ALL CONDUITS TO BE INSTALLED IN ACCORDANCE WITH LOCAL ELECTRICAL CODES.
3. REPLACE TUBING AND SHIELDING WHERE NECESSARY TO PROTECT FROM DAMAGE TO PLANTS TO BE REPLACED. CONTRACTOR TO VERIFY QUANTITIES AND PLANT SIZE.
4. SEE SEE PROJECTION DIMENSIONS WORKSHEET ON SHEETS FOR DIMENSIONS AT EXISTING PLANT MATERIAL.

**HAMILTON + ATKIN ARCHITECTS**  
 500 N. MARKET ST. SUITE 100  
 P.O. BOX 1000  
 MOUNTAIN VIEW, CA 94040  
 TEL: 925.536.3500  
 WWW.HAARCHITECT.COM

Drawn by: \_\_\_\_\_

| NO. | DESCRIPTION        | DATE     |
|-----|--------------------|----------|
| 1   | ISSUED FOR PERMITS | 08/20/20 |
| 2   | ISSUED FOR PERMITS | 08/20/20 |
| 3   | ISSUED FOR PERMITS | 08/20/20 |
| 4   | ISSUED FOR PERMITS | 08/20/20 |
| 5   | ISSUED FOR PERMITS | 08/20/20 |
| 6   | ISSUED FOR PERMITS | 08/20/20 |
| 7   | ISSUED FOR PERMITS | 08/20/20 |
| 8   | ISSUED FOR PERMITS | 08/20/20 |
| 9   | ISSUED FOR PERMITS | 08/20/20 |
| 10  | ISSUED FOR PERMITS | 08/20/20 |

THE DRAWING IS A PRELIMINARY DESIGN OF THE PROJECT AND IS NOT TO BE USED FOR CONSTRUCTION. THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS AND CONDITIONS OF THE SITE AND SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS.

# Imai Elementary School

## Portable Project

- Includes purchase and installation of one (1) 30'x32' classroom portable and associated sitework.
- Scheduled for June 2022 to August 2022.

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

# Imai (cont'd)

## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.

## Paving Project

- Onsite work scheduled to begin in June and will include resurfacing and restriping of existing blacktop play space and seal coat of existing asphalt between classroom wings.



# Imai Surveillance Camera Project



|  |  |
|--|--|
|  |  |
| 18 1/2" x 11" Map<br>Date: 03/01/2022<br>Project: IMAI<br>Prepared by: [Name]<br>Checked by: [Name]<br>Approved by: [Name] |  |
| MOUNTAIN VIEW<br>WHISMAN SD - AMY IMAI<br>ES   |  |
| AMY IMAI ES<br>253 MARTENS AVE<br>MOUNTAIN VIEW, CA<br>94040   |  |
| 75% CD   |  |
| DATE: 03/01/2022<br>DRAW NUMBER: CAC202001<br>DRAWN BY: [Name]<br>CHECKED BY: [Name]<br>DATE: 03/01/2022                   |  |
| 75% CD   |  |

Mountain View Whisman School District





# Landels Elementary School

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.





# Mistral Elementary School

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.





# Monta Loma Elementary School

## Solar Project

- Scope of work includes installation of rooftop and ground mounted solar arrays, one (1) EV charging station with 2 ports and associated equipment.
- Onsite work scheduled to begin in June 2022 and run through December 2022.

## HVAC Upgrades

- Replacement of existing HVAC units in classrooms and administration building.
- Scheduled for June 2022 to August 2022.

# Monta Loma (cont'd)

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.


## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.

# Monta Loma Solar Project

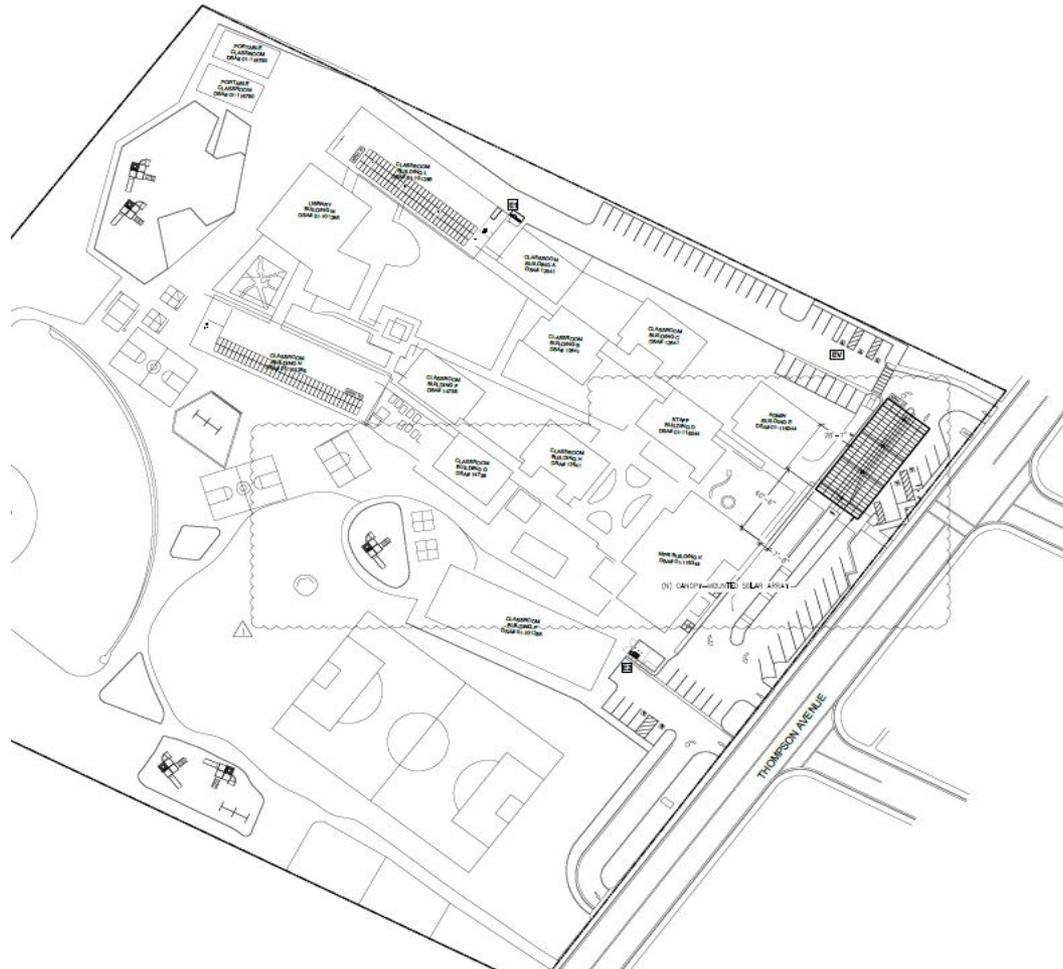

## PROJECT SUMMARY

SOLAR MODULE: LG450N2H-EI (450W)  
 PEAK POWER/STRING: 450W x 18 PANELS = 8.1KW

## PROJECT PARAMETERS

| ARRAY        | PANELS     | STRING    | POWER (KW)    |
|--------------|------------|-----------|---------------|
| R1           | 90         | 5         | 40.50         |
| R2           | 72         | 4         | 32.40         |
| R3           | 180        | 9         | 72.90         |
| <b>TOTAL</b> | <b>324</b> | <b>18</b> | <b>145.80</b> |

## SYSTEM 1 SUMMARY

|                           |   |
|---------------------------|---|
| PROJECT LOCATION          | MONTA LOMA ES<br>460 THOMPSON AVE.<br>MOUNTAIN VIEW, CA 94040 |
| MIN DESIGN TEMPERATURE    | 27C   |
| MAX 2% DESIGN TEMPERATURE | 27C   |
| PV MODULE                 | LG450N2H-EI   |
| PV MODULE VATTAGE @ STC   | 450   |
| DC SYSTEM SIZE            | 72.9KW/DC   |
| AC SYSTEM SIZE            | 80 KW/80 KW   |
| INVERTER TYPE & COUNT     | (1) CPS SCANDIT-0005-80 (80 KW)                               |

## SYSTEM 2 SUMMARY

|                           |   |
|---------------------------|---|
| PROJECT LOCATION          | MONTA LOMA ES<br>460 THOMPSON AVE.<br>MOUNTAIN VIEW, CA 94040 |
| MIN DESIGN TEMPERATURE    | 27C   |
| MAX 2% DESIGN TEMPERATURE | 27C   |
| PV MODULE                 | LG450N2H-EI   |
| PV MODULE VATTAGE @ STC   | 450   |
| DC SYSTEM SIZE            | 72.9KW/DC   |
| AC SYSTEM SIZE            | 80 KW/80 KW   |
| INVERTER TYPE & COUNT     | (1) CPS SCANDIT-0005-80 (80 KW)                               |



## PROJECT LOCATION

MONTA LOMA  
 ELEMENTARY SCHOOL  
 460 THOMPSON AVE.  
 MOUNTAIN VIEW, CA 94043

## ENGINEER



## CONSULTANT



## ENGINEER/OWNER



## ISSUE

| NO. | DATE       | DESCRIPTION             |
|-----|------------|-------------------------|
| 1   | 04/05/2023 | ISSUE FOR PERMIT REVIEW |
| 2   | 05/06/2023 | ISSUE FOR PERMIT REVIEW |
| 3   | 05/28/2023 | ISSUE FOR PERMIT REVIEW |
| 4   | 11/15/2023 | ISSUE FOR PERMIT REVIEW |
| 5   | 12/06/2023 | ISSUE FOR PERMIT REVIEW |
| 6   | 03/03/2024 | ISSUE FOR PERMIT REVIEW |

## REVISIONS

| NO. | DATE | DESCRIPTION |
|-----|------|-------------|
| 1   |      |             |
| 2   |      |             |
| 3   |      |             |
| 4   |      |             |
| 5   |      |             |

DRAWN BY: OW  
 CHECKED BY: AC  
 SCALE: 1" = 40'-0"

## REVISIONS

# Monta Loma HVAC Upgrades

located on plot is at least 48 in wide, 6'-0" minimum. The maximum slope in the 1' radius shall be 1:50. Accessible path use of overhead obstructions to 6'0" protruding more than 1' from the wall over the hand. Architect shall verify that all of travel.

indicates building included as part of this 4 way also occur in other buildings as complete utility and communication.

|  |  |
|--|--|
| <ul style="list-style-type: none"> <li>Type V-10, Class A Roof</li> <li>Area - 21,923 sf</li> <li>Not sprinkled</li> </ul> | <ul style="list-style-type: none"> <li>Type V-10, Class A Roof</li> <li>Area - 21,923 sf</li> <li>Not sprinkled</li> </ul> |
|--|--|

**Building C:**

- OSC - E
- Type V-10, Class A Roof
- Area - 22,472 sf
- Not sprinkled

**Building D:**

- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled

**Building E:**

- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled

**Building F:**

- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled

**Building G:**

- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled

**Building H:**

- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled

**Building I:**

- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled


**Building J:**

- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled

**Building K:**


- OSC - E
- Type V-10, Class A Roof
- Area - 21,923 sf
- Not sprinkled

The occupancy of existing structures as described show continue without change per the approved DSA application numbers for each building (OSC 102.5). No occupancy change, significant alteration, or increase in square footage is proposed for this project scope of work. Building is not require the addition of sprinkler. Existing building conditions, construction type, will be maintained.

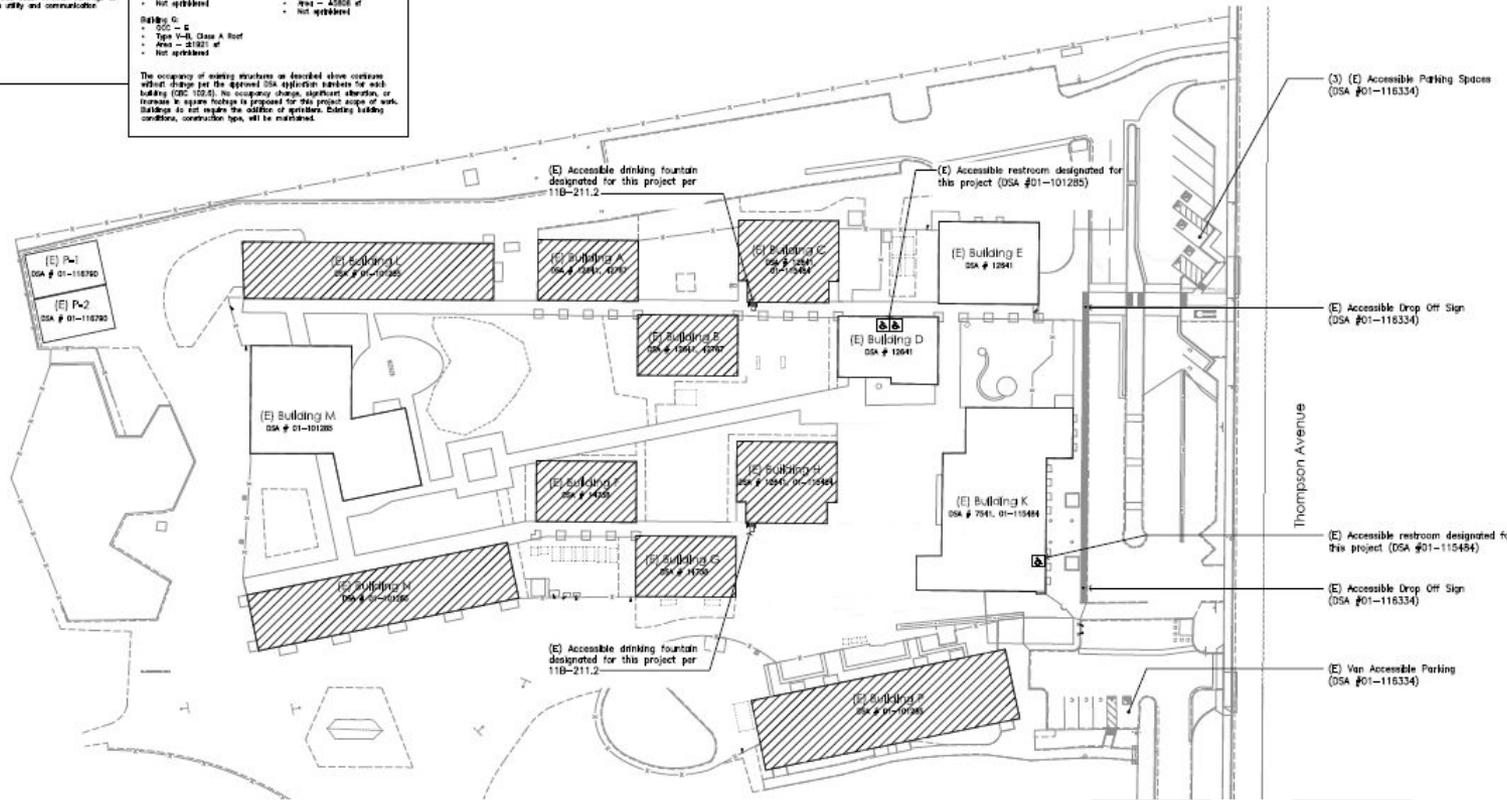

HVAC Modernization and Replacement  
**Monta Loma Elementary School**  
 4453 Thompson Ave  
 Mountain View, CA 94042

# Monta Loma Surveillance Camera Project

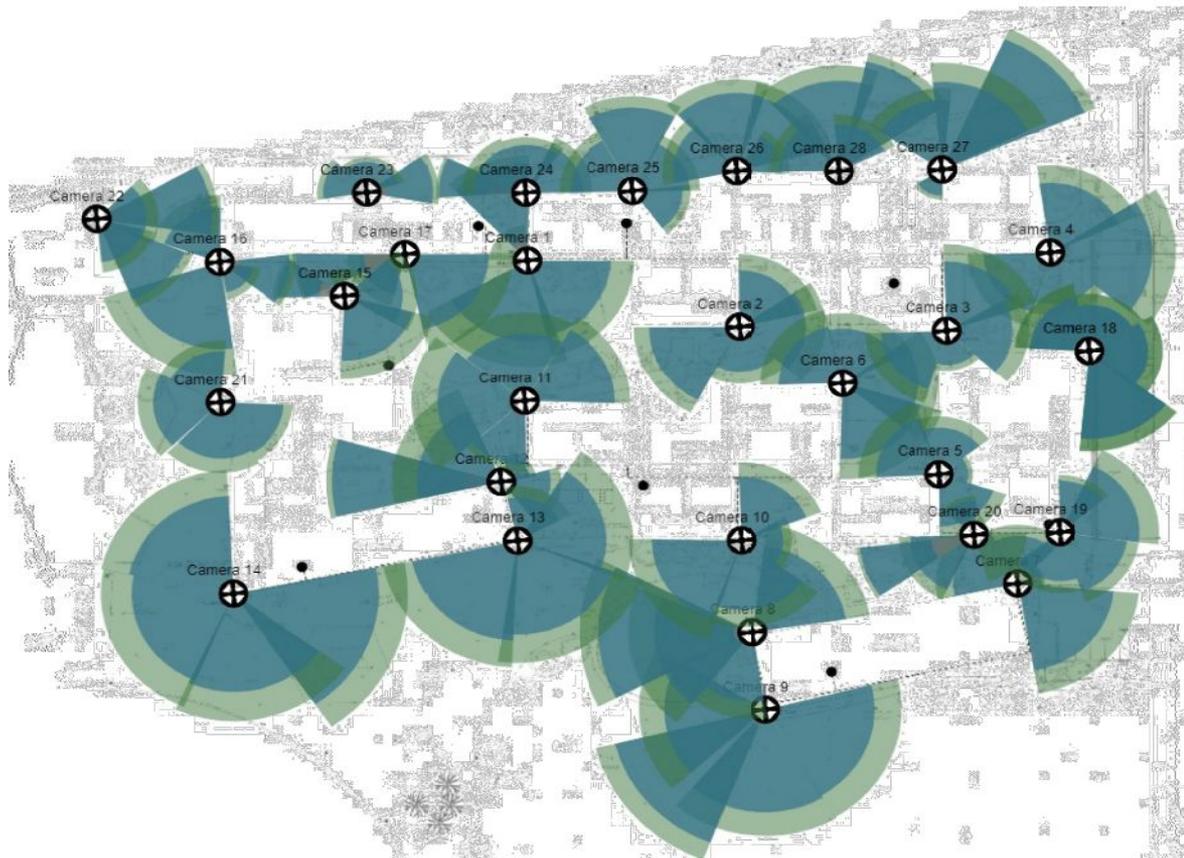

|  |        |
|--|--------|
|  |        |
| 18000 S. ...<br>...<br>...                                   |        |
| MOUNTAIN VIEW<br>WHISMAN SD - MONTA<br>LOMA ES               |        |
| MONTA LOMA<br>460 THOMPSON AVE<br>MOUNTAIN VIEW, CA<br>94043 |        |
| ...  |        |
| NO.  |        |
| ...  |        |
| DATE   | 7/5/11 |
| TIME   | ...    |
| DATE   | ...    |
| DESCRIPTION  | ...    |
| 75% CD   |        |
| DATE   | ...    |
| CASE NUMBER  | ...    |
| PROJECT  | ...    |
| DESIGNED BY  | AM     |



# Stevenson Elementary School

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

## Site Lighting

- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.





# Theuerkauf Elementary School

## Solar Project

- Scope of work includes installation of rooftop and ground mounted solar arrays, one (1) EV charging station with 2 ports and associated equipment.
- Onsite work scheduled to begin in June 2022 and run through December 2022.

## HVAC Upgrades

- Replacement of existing HVAC units in classrooms and administration building.
- Scheduled for June 2022 to August 2022.

# Theuerkauf (cont'd)

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.


## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.

## Site Lighting


- Scope of work includes installation of site lighting to illuminate path of travel from parking and entry points to classrooms and offices.
- Construction scheduled for June 2022 to August 2022.

# Theuerkauf Solar

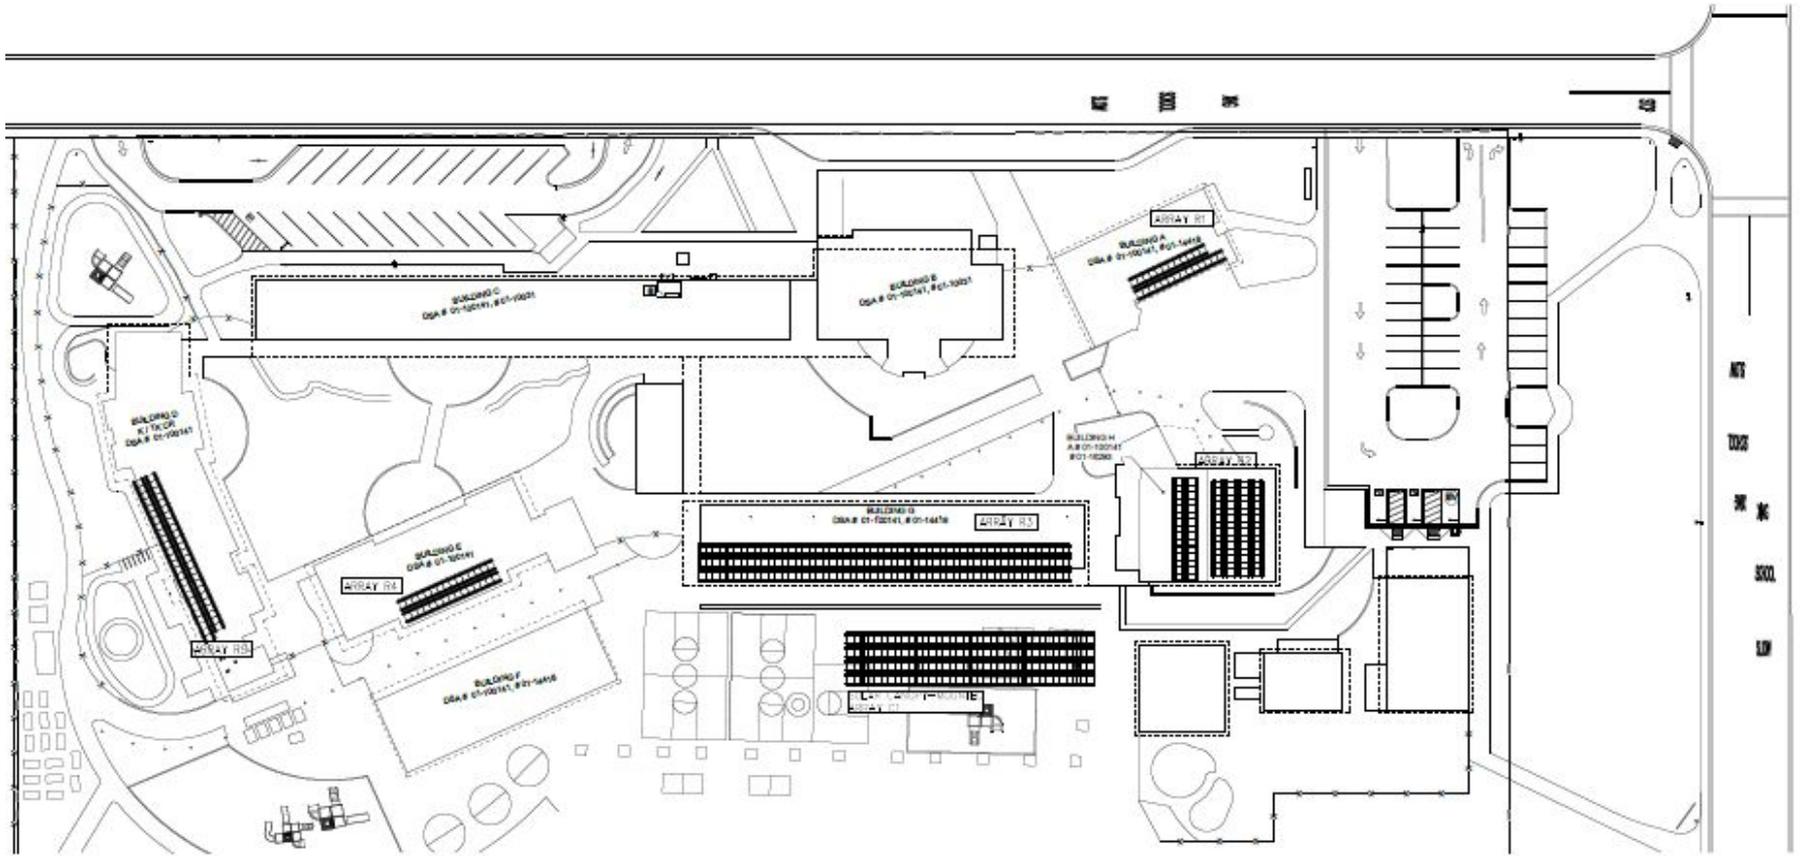



# Theuerkauf Surveillance Camera Project

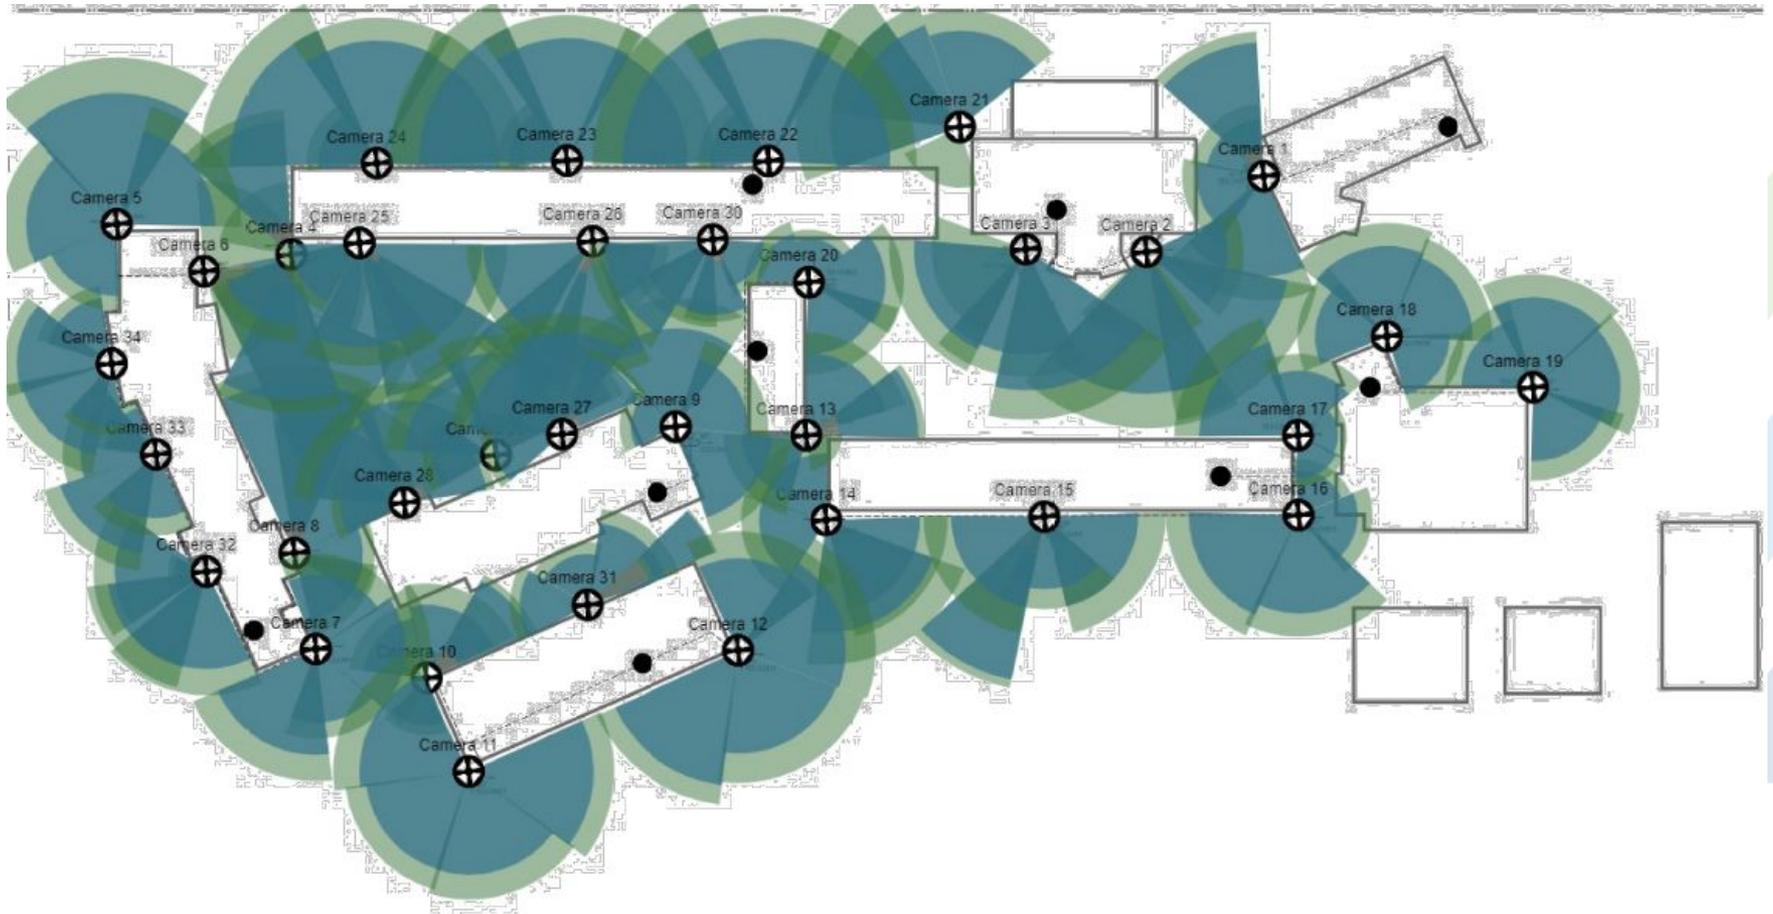



# Vargas Elementary School

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.


## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.


## Parking Cover Project

- Includes installation of custom canopy parking cover to protect pedestrians and vehicles from falling debris from trees above parking area.
- Construction is scheduled for June 2022 to August 2022.

# Vargas Surveillance Camera Project

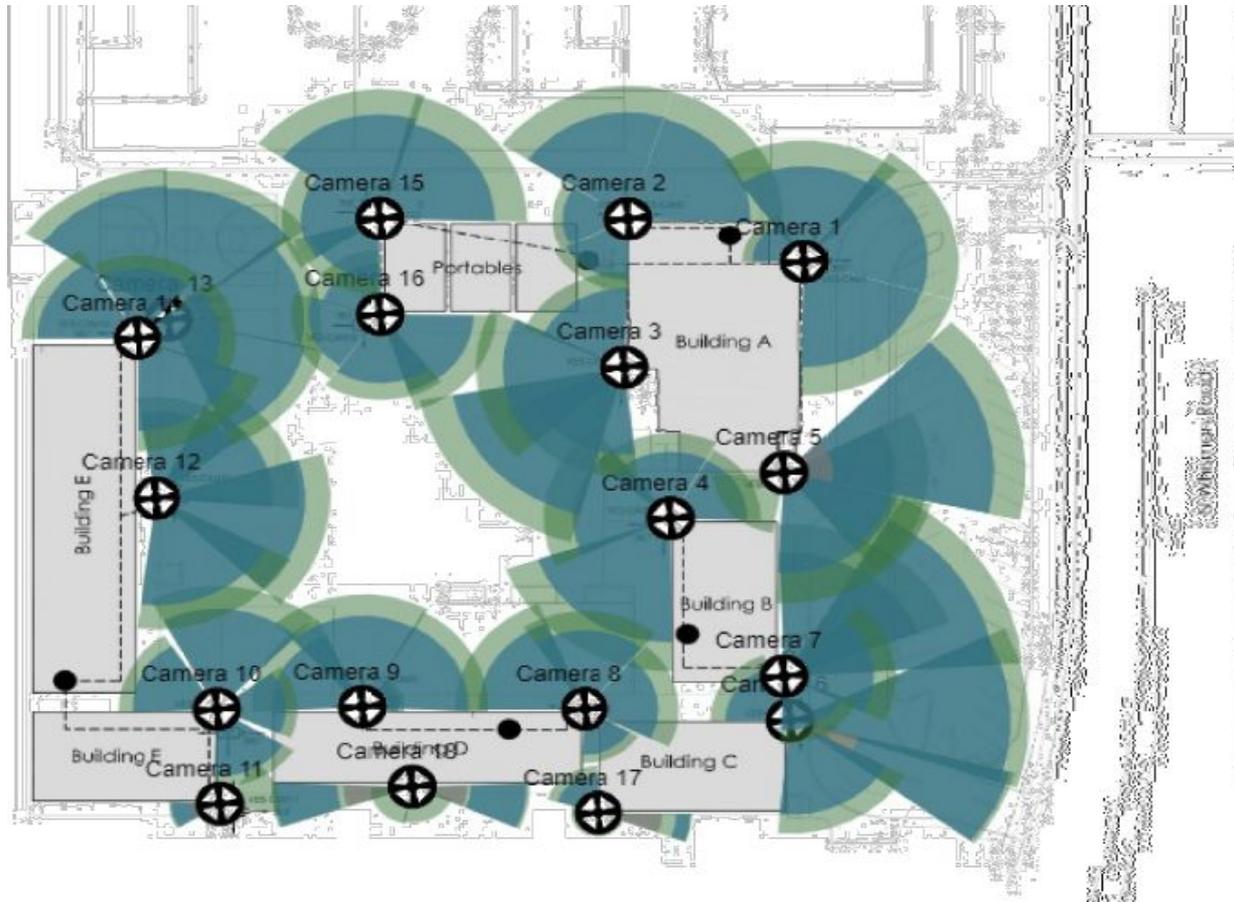

# Vargas Parking Cover

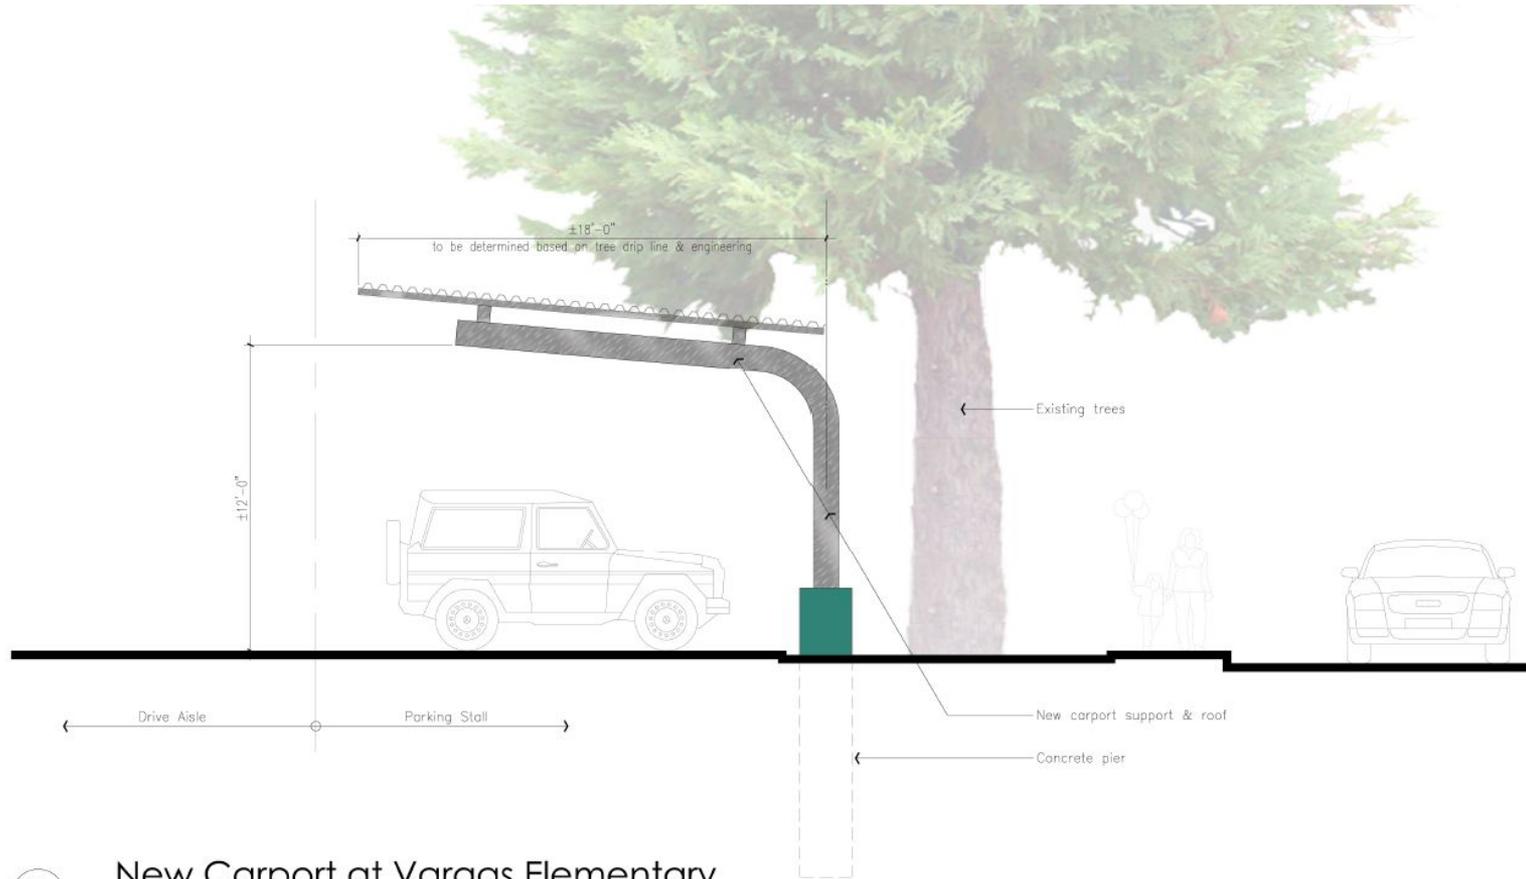

1 New Carport at Vargas Elementary

DTA Dreiling Terrones Architecture Inc.  
Architecture | Infrastructure | Environments

# District Office Building

## Access Control Project

- Work will include installation of card readers and associated equipment for electronic access of classrooms and office spaces.
- Planned to begin in July 2021 and be completed by January 2023. Work to install equipment will take place during normal business hours during summer of 2022 and move to after hours work once classes resume in August.

## Surveillance Camera Project

- Scope of work includes installation of surveillance cameras and associated equipment in accordance with the Board approved camera policy.
- Construction is scheduled for June 2022 to September 2022.



# Employee Housing Project

- Demolition of existing buildings is nearly complete.
- District and Developer are in negotiations on final construction contract amount and terms which will be brought to the Board of Trustees for approval.

# Projects Projected to begin Construction in Fall 2022

- Storage Buildings at Stevenson and Vargas Elementary Schools
- Crittenden and Theuerkauf Electrical Upgrades
- Park Restroom Buildings at Castro, Imai and Landels Elementary Schools
- Window Replacement Project Phase 1 - Installation of operable windows at Castro Elementary, Stevenson Elementary School and the District Office. Work is planned for off hours
- HVAC Upgrades Phase 3 Project - Includes replacement of HVAC units at Library/SPED Buildings at Bubb, Imai and Landels Elementary Schools

# Projects Currently in Design

- Window Replacement Project Phase 2
- Vargas Elementary School MUR Roll Up Door Project



Mountain View  
Whisman  
School District

# Questions?
